

From: (b)(6); (b)(7)(C)
Sent: 15 May 2020 13:15:44 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: (b)(7)(E) ERO Scarborough.
Attachments: (b)(7)(E)
Guidance for HSI Special Agents and Task Force Officers, Excerpt from Jury Instructions.pdf, Portland ME
HSI Processing Workstations ICEOCIOAHL.xlsx

(b)(6);
(b)(7)(C)

Forgot to copy you. Please read the first email below (b)(7)(E) from (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O: 305-597-
C: 202-754-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Friday, May 15, 2020 9:06 AM
To: (b)(6); (b)(7)(C)
Cc:
(b)(6); (b)(7)(C)
Subject: FW: (b)(7)(E) ERO Scarborough.

Good Morning (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C); (b)(5); (b)(7)(E)

Thank you in advance for your help.

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Friday, May 15, 2020 7:47 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: (b)(7)(E)

(b)(5); (b)(6); (b)(7)(C); (b)(7)(E)

Thanks,

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, May 14, 2020 3:12 PM
To: (b)(6); (b)(7)(C)
Subject: FW: (b)(7)(E)

(b)(6);
(b)(7)(C)

Please see below. This ICE policy applies to HSI criminal investigators. (b)(5)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780 (b)(6); (b)(7)(C)
Desk Phone#: 207-80 (b)(6); (b)(7)(C)
Cell Phone#: 207-252 (b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an~~

~~authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~


From: (b)(6); (b)(7)(C)
Sent: Wednesday, May 13, 2020 1:02 PM
To: (b)(6); (b)(7)(C)
Subject: (b)(7)(E)

(b)(6);
(b)(7)(C)

(b)(5); (b)(7)(E)



(b)(6); (b)(7)(C)



*(A) Resident Agent in Charge
Homeland Security Investigations
Portland, Maine
Office- 207-541- (b)(6); (b)(7)(C)
Mobile- 617-272- (b)(6); (b)(7)(C)*

(b)(6); (b)(7)(C)



(b)(6), (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 25 Jun 2019 18:28:45 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: ICE - ERO Scarborough ME, 40 Manson Libby Rd
Importance: High

Hi (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
OAFM Project Manager
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW. (b)(6); (b)(7)(C)
Washington, DC 20536
O: 202-732-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6), (b)(7)(C)
Sent: 17 Feb 2021 14:22:51 +0000
To: (b)(6), (b)(7)(C)
(b)(6), (b)(7)(C)
Cc: (b)(6), (b)(7)(C)
Subject: ICE Scarborough ME - Construction Schedule
Attachments: 2.11.21_40 Manson Libby Schedule.pdf
Importance: High

To all,

Attached please find the GC updated schedule.

Special attention to the wall inspections date and the furniture measurements.

90	GSA In Wall Inspection	0 days	Fri 3/12/21	Fri 3/12/21
91	Insulation & Drywall	20 days	Mon 3/15/21	Fri 4/9/21
92	Bathroom Tile	10 days	Mon 3/22/21	Fri 4/2/21
93	Bathroom Partitions	5 days	Mon 4/5/21	Fri 4/9/21
94	GSA Field Measure - Furniture	0 days	Mon 4/12/21	Mon 4/12/21

Let me know if you have any questions or concerns.

Thank you,

(b)(6), (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
1	Preconstruction	137 days	Wed 5/13/20	Thu 11/19/20	
8	Mobilization	4 days	Fri 11/6/20	Wed 11/11/20	
13	Sitework	34 days	Mon 11/9/20	Thu 12/24/20	
30	Site Completion	TBD	TBD	TBD	
31	Site Demo & Removal	1 day	Mon 4/19/21	Mon 4/19/21	
32	Box cut parking area	10 days	Mon 4/19/21	Fri 4/30/21	
33	Gravel & Grade	10 days	Mon 4/19/21	Fri 4/30/21	
34	Install Fencing	8 days	Wed 5/19/21	Fri 5/28/21	
35	Remaining Bollards	10 days	Mon 4/19/21	Fri 4/30/21	
36	Curbing	3 days	Wed 5/19/21	Fri 5/21/21	
37	Binder Pave	2 days	Mon 5/17/21	Tue 5/18/21	
38	Landscaping	5 days	Mon 5/24/21	Fri 5/28/21	
39	Finish Pave	4 days	Mon 5/31/21	Thu 6/3/21	
40	Signage & Markings	1 day	Thu 6/4/20	Thu 6/4/20	
41	Foundations	20 days	Thu 11/19/20	Wed 12/16/20	
42	Form Footings	2 days	Thu 11/19/20	Fri 11/20/20	19FS-1 day
43	Rebar Inspection	1 day	Fri 11/20/20	Fri 11/20/20	42FS-1 day
44	Place Footers	1 day	Fri 11/20/20	Fri 11/20/20	43FS-1 day
45	Form Walls	2 days	Mon 11/23/20	Tue 11/24/20	44
46	Rebar Inspection	1 day	Wed 11/25/20	Wed 11/25/20	45
47	Place Walls	1 day	Wed 11/25/20	Wed 11/25/20	46FS-1 day
48	Prep Entry Slabs	3 days	Wed 12/2/20	Fri 12/4/20	
49	Rebar Inspection	1 day	Fri 12/4/20	Fri 12/4/20	48FS-1 day
50	Place Entry Slabs	1 day	Fri 12/4/20	Fri 12/4/20	49FS-1 day
51	Form Site Slabs	4 days	Mon 4/19/21	Thu 4/22/21	
52	Rebar Inspection	1 day	Thu 4/22/21	Thu 4/22/21	51FS-1 day
53	Place Site Slabs	2 days	Fri 4/23/21	Mon 4/26/21	52FS-1 day
54	Interior Demolition	5 days	Wed 9/16/20	Tue 9/22/20	
58	Underslab Activities	26 days	Mon 11/9/20	Mon 12/14/20	
69	Exterior Wall Demo	29 days	Tue 12/15/20	Fri 1/22/21	
74	Masonry	46 days	Mon 1/4/21	Mon 3/8/21	
75	Ext CMU	27 days	Mon 1/4/21	Tue 2/9/21	73FS-10 days
76	Int CMU	20 days	Wed 2/10/21	Tue 3/9/21	75FS-20 days
77	Exterior Openings & Roofing	25 days	Mon 2/15/21	Fri 3/19/21	
78	Sectional Doors	5 days	Mon 3/15/21	Fri 3/19/21	
79	Storefronts & Windows	3 days	Mon 3/15/21	Wed 3/17/21	
80	Roofing	25 days	Mon 2/15/21	Fri 3/19/21	
81	Interior Fit Up	86 days?	Thu 12/17/20	Thu 4/15/21	
82	HVAC Duct & RTU penetrations	13 days	Mon 3/8/21	Wed 3/24/21	
83	Cable tray	13 days	Mon 2/22/21	Wed 3/10/21	
84	CMU Wall Pathways/MEP coordinatic	20 days	Wed 2/10/21	Tue 3/9/21	



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
85	LGMF & Door Frames	18 days	Mon 2/22/21	Wed 3/17/21	75FS-18 days
86	Frame Processing Desk	5 days	Mon 3/1/21	Fri 3/5/21	
87	Blocking	13 days	Mon 2/22/21	Wed 3/10/21	
88	MEP & Comm/Security Rough	10 days	Mon 3/1/21	Fri 3/12/21	85FS-13 days
89	MEP Inspection	1 day	Fri 3/12/21	Fri 3/12/21	
90	GSA In Wall Inspection	0 days	Fri 3/12/21	Fri 3/12/21	88
91	Insulation & Drywall	20 days	Mon 3/15/21	Fri 4/9/21	90
92	Bathroom Tile	10 days	Mon 3/22/21	Fri 4/2/21	
93	Bathroom Partitions	5 days	Mon 4/5/21	Fri 4/9/21	
94	GSA Field Measure - Furniture	0 days	Mon 4/12/21	Mon 4/12/21	91FS+1 day
95	Prime & First Coat Paint	8 days	Mon 4/12/21	Wed 4/21/21	91
96	Ceiling Grid & Cuts	8 days	Thu 4/15/21	Mon 4/26/21	95FS-5 days
97	MEP Finishes	8 days	Fri 4/16/21	Tue 4/27/21	95FS-4 days
98	Flooring	7 days	Mon 5/3/21	Tue 5/11/21	95
99	Epoxy Flooring	2 days	Thu 5/6/21	Fri 5/7/21	
100	SS at Processing	10 days	Thu 4/22/21	Wed 5/5/21	
101	Casework	3 days	Thu 4/15/21	Mon 4/19/21	95FS-5 days
102	Flood Ceilings	5 days	Wed 4/28/21	Tue 5/4/21	97
103	Specialites & Furnishings	3 days	Wed 5/12/21	Fri 5/14/21	98
104	Doors & Hardware	3 days	Wed 5/12/21	Fri 5/14/21	98
105	Conference Room Door & Glass	3 days	Wed 5/12/21	Fri 5/14/21	
106	Final Paint	3 days	Wed 5/12/21	Fri 5/14/21	98
107	Signage	2 days	Wed 5/12/21	Thu 5/13/21	106FS-3 days
108	Cleaning	2 days	Thu 5/13/21	Fri 5/14/21	107FS-2 days
109	Substantial Completion	0 days	Fri 5/14/21	Fri 5/14/21	108
110	Closeout	15 days	Mon 5/17/21	Fri 6/4/21	
111	Punchlist	15 days	Mon 5/17/21	Fri 6/4/21	109
112	Final Inspection - GSA	1 day	Fri 6/4/21	Fri 6/4/21	111FS-1 day
113	Occupancy & Turnover	0 days	Fri 6/4/21	Fri 6/4/21	112
114					
115					

From: (b)(6); (b)(7)(C)
Sent: 11 Feb 2021 14:21:32 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: ICE Scarborough ME - Executed Lease
Attachments: LME00266_Lease_-_Executed_Lease_-_Executed_8_22_2019 (3).pdf
Importance: High

(b)(6);
(b)(7)(C)

Attached is a copy of the executed lease for your records.
Please let me know if you need any other additional information.

Thank you,

(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 27 Jan 2021 21:11:10 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: ICE Scarborough ME - Move/Dispose of from 176 Gannett Drive, South Portland, ME.to 40 Mason Libby Rd. Scarborough, ME.
Attachments: HSI PORTLAND Inventory - Move Matrix.xlsx
Importance: High

Good morning (b)(6); (b)(7)(C)

In preparation for your move, I will need a list of items that need to be moved and a list of disposed items from 176 Gannett Drive .to 40 Mason Libby Rd.
Attached please find a sample excel sheet that we used when HSI moved to One City Center.

Do not hesitate to contact me if you have any questions or concerns.

Thank you.

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location	Item	New Location	Dimensions
4				
5	201	Secure Fax	019	16x16x13
6	201	Secure Phone	019	11x10x9
7	201	Personal Items	005	4 boxes
8	201	Docking Station	?	1 box
9	201	2 monitors		2 monitors
10	201	Supply Closet	017	25 boxes
11				
12				
13	202	OCIO Equip	008	80x40x24
14				
15	203	Flag and Flag Stand	006	
16	203	42" TV	022	43x24x8
17	203	Framed Art and Plaques	006	25x18x18
18	203	42" TV		43x24x8
19				
20	204	Secure Shredder	007	30x18x12
21	204	Docking station and scanner	007	1 box
22	204	Monitors	007	2 monitors
23				
24				
25				
26	205	Shredder	004	39x25x24
27	205	Fax Machine	004	15x14x14
28	205	Network Color Printer	004	18x18x14
29	205	Radio Consolette and Table	017	30x27x20
30	205	Standalone Copier	004	55x28x28
31	205	Tall beige Cabinet	017	78x36x18
32	205	Tall beige Cabinet	017	78x36x18
33	205	Evidence supplies	016	2 boxes
34	205	Ink Supplies	017	2 boxes
35				
36				
37	206	Case Files	017	75 boxes
38	206	Tech Ops Equip	017	78x36x18
39	206	Black 4 drawer lateral cab	017	52x44x18
40				
41				
42	212	(b)(6); (b)(7)(C) Personal items	008	2 boxes
43	212	(b)(6); (b)(7)(C) Printer and Docking Station	008	1 box
44	212	(b)(6); (b)(7)(C) 4 Computer Monitors	?	4 Monitors
45	212	(b)(6); (b)(7)(C) Personal items	?	2 boxes

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location/	Item	New Location	Dimensions
4	Conf room	Sharp monitor		37"
5	Conf room	Toshiba TV		36"
6	Hallway	Sharp TV		31"
7				
8				
9	Supply room	CS637037 Kyocera copier/printer		48"x50"x29"
10	Supply room	Shredder		34"x17.5"x17"
11	Supply room	50 boxes supplies		18x18.5x16
12	RAC office	Toshiba TV		22"
13				
14	RAC office	STE phone		5 lbs
15	RAC office	Panasonic secure fax		11"x22"x15"
16	RAC office	20 boxes case files		standard
17	RAC office	2 boxes misc items		18x18.5x16
19	Closet	11 boxes of printer paper		standard
20				
21				
22	Tech room	1 Pelican case		24"x15"x10"
23	Tech room	1 Pelican case		19"x14"7"
24	Tech room	1 equipment bag		24"x14"x15"
25	Tech room	20 boxes misc equipment		18x18.5x16
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location / Middle Street	Item	New Location	Dimensions
4	Middle St. Kitchen	Folding Table	TBD	6'x30"
5	Middle St.	2 boxes	Kitchen	
6	Middle St.	Evidence Boxes	Evidence	24"x24"x8"
7	Middle St. Common Area	Brother Printer	UC Room	18"x17"x18"
8	Middle St. Common Area	Printer Cart	UC Room	24"x18"x36"
9	Middle St. Common Area	Monitor	TBD	37"
10	Middle St. Common Area	Monitor	TBD	60"
11	Middle St. Common Area	Glass White Board	TBD	6'x4'
12	Middle St. IT Room	7 boxes	Bulk Storage	
13	Middle St. IT	HP Printer	Printer	22"x22"x17"
14	Middle St. Grand Jury Room	20 Boxes	Grand Jury Room	
15	Middle St. Computer	MacPro Computer	Computer Forensics	
16	Middle St. Computer	HP Z840 Computer	Computer Forensics	
17	Middle St. Computer	iMac Computer	Computer Forensics	
18	Middle St. Computer	Pegasus Storage Device	Computer Forensics	
19	Middle St. Computer	Drobo Storage Device	Computer Forensics	
20	Middle St. Computer	Samsung Monitor	Computer Forensics	24"
21	Middle St. Computer	Acer Monitor	Computer Forensics	28"
22	Middle St. Computer	HP Monitor	Computer Forensics	28"
23	Middle St. Computer	20 Boxes	Computer Forensics	
24	Middle St. Computer	9 Hard Sided Plastic Cases	Computer Forensics	
25	Middle St. Supply Room	25 Boxes	Bulk Storage	
26	Middle St. Supply Room	2 HP Printers	Computer Forensics	15"x21"x19"
27				
28				
29				
30				
31				
32				

33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location	Item	New Location	Dimensions
4	SOPO Office	Desk Chair		Standard Size
5	SOPO Office	Two Computer Monitors		21"X13"X2.5"
6	SOPO Office	Snapscan Scanner		12"X6"X6"
8	SOPO Office	Fan		8"X10"X6"
9	SOPO Office	Two Filing Cabinet		16"X30"X30"
10	SOPO Office	Twelve Office Box Supplies		18.5"X18"X16"
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location	Item	New Location	Dimensions
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location	Item	New Location	Dimensions
4	Middle Office # 1	Uplift Desk and floor mat	425	5ft x 5ft
5	Middle Office # 1	computer monitor	425	26x18x.5
6	Middle Office # 1	Personal Items	425	10 Boxes
7	Middle Office # 1	TV Monitor	425	38x32x2
8	Middle Office # 1	computer monitor	425	25x15x.5
9	Middle Office # 1	computer monitor	425	22x13x1
10	Middle Office # 1	Large filing cabinet	425	3ftx4.5ftx2ft
11	Middle Office # 1	10 boxes: Office Supplies / Files etc	425	18.5x18x16
12	Middle Office # 1	White board	425	6ft x 4ft
13	Middle Office # 1	Coat rack	425	5.5ft x 1ft
15	Middle Office # 1	Small filing cabinet (2)	425	15x29x28
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A		C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location		New Location	Dimensions
4	Middle St	15 Boxes: Office supplies/files etc.		18.5"x18"x16"
5	Middle St	Sit-Stand Desktop		40"x28"x5"
6	Middle St	Tall Office Chair		54"x27"x27"
7	Middle St	Computer monitor		22"x13"x2.5"
8	Middle St	Computer monitor		21"x13"x2.5"
9	Middle St	Television/Monitor		35.5"x21"x3"
10	Middle St	Filing cabinet		28"x16"x22"
11	Middle St	Desk Lamp		15" x 10"
12	Middle St	Floor Lamp		5'x10"
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location	Item	New Location	Dimensions
4	Gannett Drive	Dell monitor		16"x15"
5		ViewSonic monitor		20.5"x12.5"
6		HP desktop computer		20"x16"
7		2 plastic file storage boxes		18.5x14.5x12
8		12 boxes misc/personal/case files		18.5x18x16
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location/ Middle Street	Item	New Locatio	Dimensions
4	Middle St. Office	12 Boxes	TBD	18.5"X18"X1
5	Middle St. Office	3 Cork Boards	TBD	3'x2'
6	Middle St. Office	Scanner	TBD	5lbs.
7	Middle St. Office	Computer Monitor	TBD	32"
	Middle St. Office	Computer Monitor	TBD	22"
8	Middle St. Office	Computer Monitor	TBD	23"
9	Middle St. Office	VariDesk	TBD	40"x26"
10	Middle St. Office	VariDesk Dual Monitor Arms	TBD	10lbs.
13	Middle St. Office	Viper Phone	TBD	5lbs.
15	Middle St. Office	Laptop & Docking Station	TBD	10lbs.
16	Middle St. Office	Standing Floor Mat	TBD	2'x4'
17	Middle St. Office	Wireless Router & Modem	IT	10lbs.
18	Middle St. Office			
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location /	Item	New Location	Dimensions
4		Document Scanner		14"x8"x8"
5		2 Monitors		
6		10 boxes containing case files etc.		18.5x14.5x12
7		2 boxes w/ Misc equip. Scales calculators etc.		18.5x14.5x12
8		White Board		6'x4'
9		3 diplays		6'x4'
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

	A	B	C	D
1	HSI Portland Inventory - Move Matrix			
2				
3	Current Location/	Item	New Location	Dimensions
4	Pritchard	ViewSonic Monitor	TBD	22"x13"x2.5"
5	Pritchard	ViewSonic Monitor	TBD	22"x13"x2.5"
6	Pritchard	HP Laptop	TBD	12" x 9"
7	Pritchard	Varidesk	TBD	40" x 26"
8	Pritchard	Varidesk Chair	TBD	30" tall
9	Pritchard	Varidesk Floor Mat	TBD	2' x 4'
10	Pritchard	Fujitsu Scanner	TBD	14"x8"x8"
11	Pritchard	HP LaserJet Printer	TBD	18"x15"x12"
12	Pritchard	25 Boxes, Misellaneous files, etc.	TBD	18.5"x18"x16"
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				
45				

From:

(b)(6); (b)(7)(C)

Sent:

24 Feb 2021 16:34:44 +0000

To:

(b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject:

ICE Scarborough ME - Partial upper portion of the demising wall Mesh

Inspection

Importance:

High

(b)(6); (b)(7)(C)

Partial upper portion of the demising wall mesh inspection has been confirmed for Wednesday March 03, 2021 at 10 am. If you need to postpone the inspection please let us know with sufficient time.



Thank you.

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 20 Jan 2021 19:01:34 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

To all,

GSA PM contacted me today, because The GC's security contractor cannot be on the call tomorrow at 9am. They are asking if we could change it to 11am. Is that ok with you?

Please let me know.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, January 14, 2021 12:28 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

Please add the attached to your calendar.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, January 14, 2021 11:30 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

I did not receive an invite. (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, January 14, 2021 8:07 AM
To: (b)(6); (b)(7)(C)
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

Good Morning all,

I forwarded the invite to you yesterday for next Thursday January 21 at 9am. Please let me know if you have received it.

ICE Scarborough ME - Security Meeting

When Thu Jan 21, 2021 9am – 10am Eastern Time - New York

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, January 13, 2021 5:30 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

(b)(5)

Sent with BlackBerry Work

www.blackberry.com

From: (b)(6); (b)(7)(C)

Date: Wednesday, Jan 13, 2021, 8:34 AM

To: (b)(6); (b)(7)(C)

Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

(b)(5)

(b)(6); (b)(7)(C); (b)(5)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, January 13, 2021 6:52 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

(b)(6); (b)(7)(C); (b)(5)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, January 12, 2021 4:01 PM

To: (b)(6); (b)(7)(C)

Subject: 40 Manson Libby Rd - Door Hardware RFI

Importance: High

Hello (b)(6); (b)(7)(C)

The GC and the vendor have some door's hardware questions. We usually schedule a meeting with them.

What date and time works for you this week or next week for a meeting to go over the hardware RFI? I am off Friday and Monday is a holiday.

Please let me know.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager

O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 20 Jan 2021 19:10:54 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

We will leave the meeting for 9 am.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:03 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

(b)(5)

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:02 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

To all,

GSA PM contacted me today, because The GC's security contractor cannot be on the call tomorrow at 9am. They are asking if we could change it to 11am. Is that ok with you?
Please let me know.

From: (b)(6); (b)(7)(C)
Sent: 20 Jan 2021 21:04:35 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

To all,

Tomorrow's meeting for the hardware and security questions has been canceled by GSA. See note below:

*This event has been canceled with this note:
"Rescheduled for 1/26/2021 at 2:30pm after the weekly meetings call. We will be using the same number from our weekly calls. "*

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:11 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

We will leave the meeting as scheduled at 9am.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:05 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI

Does not work for me. Sorry (b)(6)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:02 PM
To: (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 28 Jan 2021 18:28:42 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

(b)(6);
(b)(7)(C)

(b)(5)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 4:05 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

To all,

Tomorrow's meeting for the hardware and security questions has been canceled by GSA. See note below:

This event has been canceled with this note:

"Rescheduled for 1/26/2021 at 2:30pm after the weekly meetings call. We will be using the same number from our weekly calls. "

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 20, 2021 2:11 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson Libby Rd - Door Hardware RFI
Importance: High

From: (b)(6); (b)(7)(C)
Sent: 26 Feb 2021 00:40:33 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: Burlington FOD-ERO February 2021 Project Call
Attachments: FOD Boston Update February 25 , 2021.pdf
Importance: High

Disregard the previous report. Attached please find the report.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAEM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, February 25, 2021 5:15 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: Burlington FOD-ERO February 2021 Project Call

See attached updated project file.

(b)(6); (b)(7)(C)
Facilities Project Manager
DHS/ Office of Asset & Facilities Management
500 12th Street, SW (b)(6); (b)(7)(C) Washington, DC 20536
O: (202) 732-(b)(6);
M: (202) 425-(b)(7)(C)



-----Original Appointment-----

From: (b)(6); (b)(7)(C)

Sent: Tuesday, June 9, 2020 1:36 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: Burlington FOD-ERO Monthly Project Status Call

When: Thursday, March 25, 2021 9:30 AM-10:00 AM (UTC-05:00) Eastern Time (US & Canada).

Where: Call

To all,

This is a series of recurring calls of Burlington FOD-ERO Projects for the fourth Thursday of each month at 1:00 pm.

Conference Call #: 1-866-692-(b)(6); (b)(7)(C)

Participant Passcode (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Facilities Project Manager

DHS/ Office of Asset & Facilities Management

500 12th Street, SW. (b)(6); (b)(7)(C) Washington, DC 20536

O: (202) 732-(b)(6); (b)(7)(C)

M: (202) 425-(b)(6); (b)(7)(C)

Project Number	Proj. Name	State	Update	Notes from call & next steps	DATE UPDATED	PM Contacts	Project Phase
PRO-13-ERO-0231	Hartford ERO	CT	No Change - Project complete. Refrigerator is able to be delivered - MSS to request funding today.	Proeject is completed in RPMS.	2/24/2021	Dan	Install/ Occupancy
PRO-17-SHD-0113	Warwick RI Lease	RI	Last week the LCO issued another rejection of the CDs. The lessor is working to provide a complete and acceptable design package before we move into the pricing phase.	Project Phase Final Design.	2/25/2021	MMM	CDs
PRO-13-ERO-0293	Scarborough ERO	ME	Construction is progresing. Partial upper demising wall mesh inspection on March 03, 2021. New construction schedule provided by GSA. Substantial completion date 05-14-21. Occupancy date 06-04-21.	Project Phase Construction	2/25/2021	MMM	Construction
PRO-18-ERO-0119	ST. ALBANS ERO OFFICE 64 GRICE BROOK ROAD	VT	Updated 15 year OA signed, lease review pending. RWA funded and accepted by GSA for the installation of a gated security fence . GSA is advising that they will start contract once the lease is signed.		2/24/2021	Judith	GSA lease action
PRO-19-ERO-0032	Burlington MA Lease Renewal & Refresh 10 New England	MA	100% CDs for the renovation of bathrooms. The lessor's construction proposal was determined fair/reasonable after review by GSA. The amended RWA amount necessary to complete the work is [REDACTED]. The existing RWA N1028706 is accepted for the amount of [REDACTED]. The difference in funding amounts to a total of [REDACTED].		2/24/2021	Judith	Construction - Bid
PRO-20-ERO-0128	Burlington MA NEW Lease	MA	OFA has received the FSR with requirements. Development of the SF-81 package in progress.		2/24/2021	Judith	Requirements

From: (b)(6); (b)(7)(C)
Sent: 2 Jul 2020 01:26:38 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: CCJ Saturday COVID-19 positive county inmate

I was advised that CCJ is having staff self quarantining, and it was suggested to get tested as well if an individual was concerned.

I will ask CCJ to share if any staff in the unit, Intake, or medical, test positive. They did tell me that to their knowledge he did not share a cell in the unit with an ICE detainee. However, at one point he was in the main tank for initial in processing with other detainees, and jail releases.

(b)(6); (b)(7)(C)
SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-808-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Wednesday, Jul 01, 2020, 8:36 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: CCJ Saturday COVID-19 positive county inmate

Please keep us all advised of any contact tracing being undertaken by CCJ. It looks like we are taking all necessary steps given a possibility of an exposure. If there was no contact with the infected inmate we need to advise our staff and our partners.

(b)(6); (b)(7)(C)

Assistant Field Office Director
Enforcement and Removal Operations
Boston Field Office
781-359 (b)(6); (b)(7)(C)
617-828 (b)(6); (b)(7)(C) (M)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)

Date: Wednesday, Jul 01, 2020, 7:46 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: CCJ Saturday COVID-19 positive county inmate

Great, thank you.

For everyone added to this email, the situation is that several of our detainees at Cumberland were in the same quarantine unit as a local detainee who tested positive for CV.

CCJ relays that masks are worn in the quarantine unit and that "out-time" is regulated for absolute minimum exposure.

At this point we have no reason to believe that our detainees were in close contact, but we will proceed keeping the safety of our officers and detainees first.

please let me know when your notifications are complete and if there is anything else we need to provide to anyone.

Thanks,

(b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Wednesday, Jul 01, 2020, 7:34 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6);
(b)(7)(C)

Subject: FW: CCJ Saturday COVID-19 positive county inmate

Please see the below list from (b)(6); (b)(7)(C) for which officers transported them to York. (b)(6); (b)(7)(C) is notifying York of the situation, (b)(6); (b)(7)(C) will handle the IGSA notifications.

- (b)(6); (b)(7)(C) Detained staff
- (b)(6); (b)(7)(C) - ATD
- (b)(6); (b)(7)(C) - Fug Ops

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Wednesday, Jul 01, 2020, 19:20
To: (b)(6); (b)(7)(C)
Subject: FW: CCJ Saturday COVID-19 positive county inmate

(b)(6); (b)(7)(C) - transported (b)(6); (b)(7)(C) on 6/29.

(b)(6); (b)(7)(C) - transported (b)(6); (b)(7)(C) on 6/30.

(b)(6); (b)(7)(C)
Supervisory Detention and Deportation Officer
DHS/ICE/ERO/Boston Field Office
Commercial Air Operations (CAO) / ICE Air Operations (IAO)
[1000 District Avenue](#)
[Burlington, MA 01803](#)
Office: (781) (b)(6); (b)(7)(C)
Cell: (781) 551 (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Date: Wednesday, Jul 01, 2020, 6:40 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: CCJ Saturday COVID-19 positive county inmate

All,

Please see the email train below.

(b)(6); (b)(7)(C); (b)(5)

Inmate (b)(6); (b)(7)(C) was not in the same housing unit during the time frames in question. (b)(6); (b)(7)(C)

“With regards to this request for information, Inmate (b)(6); (b)(7)(C) was in the same housing unit during the time frame that the other individual was there. (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Inmate (b)(6); (b)(7)(C) was in the same housing unit during the time frames in question. (b)(6); (b)(7)(C)

Inmate (b)(6); (b)(7)(C) was in the same housing unit during the time frames in question. (b)(6); (b)(7)(C)

The housing unit is our quarantine pod. Everyone wears masks and the out time is regulated for absolute minimum exposure.

It looks like he was also in the same unit during the time frames in question.

I hope I have helped.

Thanks,

(b)(6); (b)(7)(C)

SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-
Desk Phone#: 207-80-
Cell Phone#: 207-252-
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Wednesday, July 1, 2020 5:33 PM
To: (b)(6); (b)(7)(C)
Subject: RE: FW: Saturday

Thanks.

(b)(6); (b)(7)(C)

SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-
Desk Phone#: 207-808-
Cell Phone#: 207-252-
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Wednesday, July 1, 2020 5:31 PM
To: (b)(6); (b)(7)(C)
Subject: Re: FW: Saturday

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

It looks like he was also in the same unit during the time frames in question.

(b)(6);
(b)(7)(C)

On Wed, Jul 1, 2020 at 4:50 PM (b)(6); (b)(7)(C) wrote:

(b)(6); (b)(7)(C)

Attached is the sheet from (b)(6); (b)(7)(C) on Monday AM. What about: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780- (b)(6); (b)(7)(C)
Desk Phone#: 207-808- (b)(6); (b)(7)(C)
Cell Phone#: 207-252- (b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Wednesday, July 1, 2020 4:25 PM
To: (b)(6); (b)(7)(C)
Subject: Re: FW: Saturday

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

The inmate in question was brought in @ 0015. Officers that brought in [redacted] on 6/28/2020 @ 2257 so the inmate in question was not in custody as of that time frame.

R [redacted]
(b)(6);
(b)(7)(C)

On Wed, Jul 1, 2020 at 4:13 PM [redacted] wrote:

Thanks [redacted] So the Immigration Officers were at CCJ prior to the COVID 19 inmate? Or was the inmate already there, but in a secure unit?

[redacted] SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780- [redacted]
Desk Phone#: 207-808- [redacted]
Cell Phone#: 207-252- [redacted]
Fax#: 207-780-3216

Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.

From: [redacted]
Sent: Wednesday, July 1, 2020 3:57 PM
To: [redacted]
Subject: Re: FW: Saturday

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

[redacted]
(b)(6);
(b)(7)(C)

With regards to this request for information, Inmate [redacted] was in the same housing unit during the time frame that the other individual was there.

Inmate [redacted] was not in the same housing unit during the time frames in question.

Inmate [redacted] was in the same housing unit during the time frames in question.

Inmate (b)(6); (b)(7)(C) was in the same housing unit during the time frames in question.

The housing unit is our quarantine pod. Everyone wears masks and the out time is regulated for absolute minimum exposure.

I hope this helps.

R (b)(6); (b)(7)(C)

On Wed, Jul 1, 2020 at 3:12 PM (b)(6); (b)(7)(C) via Intake (b)(6); (b)(7)(C) wrote:

Good afternoon,

Looking to see if the two officers below, along with any ICE detainees on Saturday, 6/27, and those detained until all left CCJ B&B, would have been potentially exposed to the COVID-19 arrest.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780 (b)(6); (b)(7)(C)
Desk Phone#: 207-80 (b)(6); (b)(7)(C)
Cell Phone#: 207-252 (b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)

Date: Wednesday, Jul 01, 2020, 3:05 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: Saturday

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

DO (b)(6); (b)(7)(C) took (b)(6); (b)(7)(C) to Cumberland County on Saturday. DO (b)(6); (b)(7)(C) texted me at 2254 that he had just dropped off the subject. Also, it looks like that subject just went to York. Let me know if you find anything out.

Number	Subject ID	Case ID	Book In Date	Book In DCO	Detention Location	Book Out Date	Release / Book Out Type	Days In Custody	Days In Facility
(b)(6); (b)(7)(C); (b)(7)(E)			07/01/2020 0001	YRK	YORK COUNTY JAIL, PA	In Custody		4	1
			06/30/2020 1147	BOS	BOSTON HOLDROOM	07/01/2020 0000	Transferred - YRK	4	1
			06/27/2020 1912	BOS	CUMBERLAND COUNTY JAIL	06/30/2020 1146	Transferred - BOS	4	3

Regards,

(b)(6); (b)(7)(C)

Supervisory Detention and Deportation Officer
Immigration and Customs Enforcement
Enforcement and Removal Operations
1 International Way
Warwick, RI 02886

Desk: (401) 734-(b)(6); (b)(7)(C)

Cell: (602) 763-(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

NOTICE: This e-mail (including any attachments) is intended for the use of the individual or entity to which it is addressed. It may contain information that is privileged, confidential, or otherwise protected by applicable law. If you are not the intended recipient or the employee or agent responsible for delivery of this e-mail to the intended recipient, you are hereby notified that any dissemination, distribution, copying, or use of this e-mail or its contents is strictly prohibited. If you received this e-mail in error, please notify the sender immediately and destroy all copies.

--

(b)(6); (b)(7)(C)

Sergeant Intake/Booking

Sheriff's Office
Cumberland County

774 (b)(6);
(b)(7)(C)



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.

--
(b)(6); (b)(7)(C)

Sergeant Intake/Booking
Sheriff's Office
Cumberland County

774 (b)(6);
(b)(7)(C)



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.

--
(b)(6); (b)(7)(C)

Sergeant Intake/Booking
Sheriff's Office
Cumberland County

774 (b)(6);
(b)(7)(C)



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.

From: (b)(6); (b)(7)(C)
Sent: 11 Mar 2021 19:28:02 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO Scarborough (b)(7)(E)
Importance: High

H (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thank you,
(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6); (b)(7)(C)
C: 202-754 (b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Thursday, March 11, 2021 2:20 PM
To: (b)(6); (b)(7)(C)
Cc:

(b)(6); (b)(7)(C)

Subject: RE: ERO Scarborough (b)(7)(E)

Sounds good to me, thanks.

(b)(6);
(b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Thursday, March 11, 2021 9:22 AM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: FW: ERO Scarborough (b)(7)(E)

Importance: High

(b)(6);
(b)(7)(C)

(b)(5); (b)(6); (b)(7)(C); (b)(7)(E)

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer Boston Field Office, Portland, ME Sub-office Enforcement and Removal Operations U.S. Immigration and Customs

Enforcement

(Office) 207-780 (b)(6); (b)(7)(C)

176 Gannett Drive

South Portland, ME 04106

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Monday, March 8, 2021 12:08 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: ERO Scarborough (b)(7)(E)

Importance: High

Hi (b)(6); (b)(7)(C)

(b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 24 Nov 2020 19:27:38 +0000
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda
Attachments: 40 Manson Libby_Schedule 11-20-2020.pdf
Importance: High

To all,

To let you know that, the Landlord's team got the building permit. Attached please find construction schedule.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, September 15, 2020 3:17 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda
Importance: High

To all,

Attached please find new construction schedule.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, June 30, 2020 2:31 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda

Importance: High

To all,

Attached please find the construction schedule for ERO-Scarborough.
Please let me know who will be attending these meetings regularly.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, June 16, 2020 2:08 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda

Importance: High

Addendum 06

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, June 9, 2020 1:41 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda

Importance: High

To all,

For our meeting today, attached construction kickoff agenda.

(b)(6); (b)(7)(C)

(b)(6);
(b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O: 305-597-
C: 202-754-



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
1	Preconstruction	137 days	Wed 5/13/20	Thu 11/19/20	
2	Notice of Award	0 days	Wed 5/13/20	Wed 5/13/20	
3	Negotiate & Execute Contract	33 days	Thu 5/21/20	Mon 7/6/20	
4	Planning Board Approval	0 days	Tue 9/15/20	Tue 9/15/20	
5	Authorized to Start Site Work	1 day	Fri 11/6/20	Fri 11/6/20	
6	Building Permit	1 day	Thu 11/19/20	Thu 11/19/20	
7	Notice to Proceed	0 days	Wed 9/16/20	Wed 9/16/20	4FS+2 days,3
8	Mobilization	4 days	Fri 11/6/20	Wed 11/11/20	
9	Mobilization	1 day	Fri 11/6/20	Fri 11/6/20	
10	Start Construction	1 day	Mon 11/9/20	Mon 11/9/20	4,5
11	Erosion Controls	1 day	Mon 11/9/20	Mon 11/9/20	10FS-1 day
12	Temp Facilities	2 days	Tue 11/10/20	Wed 11/11/20	11
13	Sitework	34 days	Mon 11/9/20	Thu 12/24/20	
14	Asphalt Cutting & Interior Trench	2 days	Mon 11/9/20	Tue 11/10/20	9
15	Sanitary Sewer	4 days	Wed 11/11/20	Mon 11/16/20	14
16	Oil Water Sep Install	1 day	Tue 11/17/20	Tue 11/17/20	15
17	Gravel & Grade Ext Trench	3 days	Tue 11/17/20	Thu 11/19/20	15
18	Pave Trench	1 day	Thu 11/19/20	Thu 11/19/20	17FS-1 day
19	Excavate Entry Doors	2 days	Wed 11/18/20	Thu 11/19/20	18FS-2 days
20	Set Bollard at OH Door	3 days	Mon 11/23/20	Wed 11/25/20	19FS+1 day
21	Set Bollards at Gas Meter	1 day	Fri 11/20/20	Fri 11/20/20	
22	Light Pole Bases & UGE and Comm	5 days	Mon 11/30/20	Fri 12/4/20	21FS+1 day
23	Backfill Entry Walls	5 days	Mon 11/30/20	Fri 12/4/20	47
24	Bollards at CIP Slabs	3 days	Mon 11/23/20	Wed 11/25/20	
25	Excavate for Site Slabs	2 days	Thu 12/3/20	Fri 12/4/20	24
26	Backfill Entry Slabs	1 day	Mon 12/7/20	Mon 12/7/20	23
27	Install Drainage	4 days	Tue 12/8/20	Fri 12/11/20	
28	Backfill Site Slabs	1 day	Mon 12/14/20	Mon 12/14/20	
29	Site Clean up	5 days	Mon 12/14/20	Fri 12/18/20	
30	Site Completion	TBD	TBD	TBD	
31	Site Demo & Removal	TBD	TBD	TBD	
32	Box cut parking area	TBD	TBD	TBD	
33	Gravel & Grade	TBD	TBD	TBD	
34	Install Fencing	TBD	TBD	TBD	
35	Remaining Bollards	TBD	TBD	TBD	
36	Curbing	TBD	TBD	TBD	
37	Binder Pave	TBD	TBD	TBD	
38	Landscaping	TBD	TBD	TBD	
39	Finish Pave	TBD	TBD	TBD	
40	Signage & Markings	TBD	TBD	TBD	
41	Foundations	20 days	Thu 11/19/20	Wed 12/16/20	



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
42	Form Footings	2 days	Thu 11/19/20	Fri 11/20/20	19FS-1 day
43	Rebar Inspection	1 day	Fri 11/20/20	Fri 11/20/20	42FS-1 day
44	Place Footers	1 day	Fri 11/20/20	Fri 11/20/20	43FS-1 day
45	Form Walls	2 days	Mon 11/23/20	Tue 11/24/20	44
46	Rebar Inspection	1 day	Wed 11/25/20	Wed 11/25/20	45
47	Place Walls	1 day	Wed 11/25/20	Wed 11/25/20	46FS-1 day
48	Prep Entry Slabs	3 days	Wed 12/2/20	Fri 12/4/20	
49	Rebar Inspection	1 day	Fri 12/4/20	Fri 12/4/20	48FS-1 day
50	Place Entry Slabs	1 day	Fri 12/4/20	Fri 12/4/20	49FS-1 day
51	Form Site Slabs	3 days	Mon 12/7/20	Wed 12/9/20	50
52	Rebar Inspection	1 day	Wed 12/9/20	Wed 12/9/20	51FS-1 day
53	Place Site Slabs	2 days	Thu 12/10/20	Fri 12/11/20	52FS-1 day
54	Interior Demolition	5 days	Wed 9/16/20	Tue 9/22/20	
55					
56	Ceilings & Walls	2 days	Wed 9/16/20	Thu 9/17/20	
57	Slabs	3 days	Fri 9/18/20	Tue 9/22/20	56
58	Underslab Activities	26 days	Mon 11/9/20	Mon 12/14/20	
59	Trenching	1 day	Mon 11/9/20	Mon 11/9/20	5
60	Plumbing Rough	6 days	Tue 11/17/20	Tue 11/24/20	59FS+5 days
61	OWS installation	2 days	Tue 11/24/20	Wed 11/25/20	
62	Electrical Rough in	3 days	Mon 11/23/20	Wed 11/25/20	6FS+1 day
63	Plumbing & Electrical Inspection	1 day	Mon 11/30/20	Mon 11/30/20	62
64	Backfill	4 days	Tue 12/1/20	Fri 12/4/20	63
65	Slab Prep	2 days	Mon 12/7/20	Tue 12/8/20	64FS-1 day
66	Pour Interior Slabs	2 days	Wed 12/9/20	Thu 12/10/20	64
67	Break Results wait time	2 days	Fri 12/11/20	Mon 12/14/20	66
68	Break Test Results	1 day	Mon 12/14/20	Mon 12/14/20	
69	Exterior Wall Demo	19 days	Tue 12/15/20	Fri 1/8/21	
70	Shoring	5 days	Tue 12/15/20	Mon 12/21/20	68
71	Roofing Demo	4 days	Tue 12/15/20	Fri 12/18/20	
72	Exter wall Demo	15 days	Mon 12/21/20	Fri 1/8/21	
73	Masonry	30 days	Mon 12/21/20	Fri 1/29/21	
74	Ext CMU	25 days	Mon 12/28/20	Fri 1/29/21	
75	Int CMU	20 days	Mon 1/4/21	Fri 1/29/21	
76	Exterior Openings & Roofing	266 days	Mon 1/18/21	Mon 1/24/22	
77	Sectional Doors	5 days	Mon 1/25/21	Fri 1/29/21	
78	Storefronts & Windows	3 days	Mon 2/1/21	Wed 2/3/21	
79	Roofing	25 days	Mon 12/21/20	Fri 1/22/21	
80	Interior Fit Up	86 days	Thu 12/17/20	Thu 4/15/21	
81	HVAC Duct & RTU penetrations	13 days	Mon 12/21/20	Wed 1/6/21	
82	Cable tray	13 days	Mon 12/21/20	Wed 1/6/21	



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
83	CMU Wall Pathways/MEP coordination	20 days	Sat 1/4/20	Thu 1/30/20	
84	LGMF & Door Frames	18 days	Wed 1/13/21	Fri 2/5/21	74FS-18 days
85	Blocking	13 days	Wed 1/13/21	Fri 1/29/21	
86	MEP & Comm/Security Rough	13 days	Wed 1/20/21	Fri 2/5/21	84FS-13 days
87	MEP Inspection	1 day	Fri 2/5/21	Fri 2/5/21	
88	GSA In Wall Inspection	0 days	Fri 2/5/21	Fri 2/5/21	86
89	Insulation & Drywall	20 days	Mon 2/8/21	Fri 3/5/21	88
90	GSA Field Measure - Furniture	0 days	Fri 3/5/21	Fri 3/5/21	89
91	Prime & First Coat Paint	10 days	Mon 3/8/21	Fri 3/19/21	89
92	Ceiling Grid & Cuts	10 days	Mon 3/22/21	Fri 4/2/21	91
93	MEP Finishes	12 days	Mon 3/22/21	Tue 4/6/21	91
94	Flooring	10 days	Mon 3/22/21	Fri 4/2/21	91
95	Casework	3 days	Mon 3/22/21	Wed 3/24/21	91
96	Flood Ceilings	5 days	Wed 4/7/21	Tue 4/13/21	93
97	Specialites & Furnishings	7 days	Mon 4/5/21	Tue 4/13/21	94
98	Doors & Hardware	7 days	Mon 4/5/21	Tue 4/13/21	94
99	Final Paint	7 days	Mon 4/5/21	Tue 4/13/21	94
100	Signage	1 day	Fri 4/9/21	Fri 4/9/21	99FS-3 days
101	Cleaning	3 days	Tue 4/13/21	Thu 4/15/21	100
102	Substantial Completion	0 days	Thu 4/15/21	Thu 4/15/21	101
103	Closeout	11 days	Fri 4/16/21	Fri 4/30/21	
104	Punchlist	10 days	Fri 4/16/21	Thu 4/29/21	102
105	Final Inspection - GSA	1 day	Fri 4/30/21	Fri 4/30/21	104
106	Turnover	0 days	Fri 4/30/21	Fri 4/30/21	105



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

Resource Names	January			February			March			April			May			June			July			
	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	
Maine Reality Advisors																						
Maine Reality Advisors,Great Falls C																						
WBRC,City Of Scarborough																						
City Of Scarborough																						
City Of Scarborough																						
WBRC,Maine Reality Advisors																						
Woods Excavating																						
Great Falls Construction																						
Woods Excavating																						
Woods Excavating																						
Woods Excavating																						
Woods Excavating[140%]																						
Woods Excavating																						
Woods Excavating																						
Woods Excavating[160%]																						
Woods Excavating[160%]																						
Woods Excavating																						
Woods Excavating																						
Woods Excavating																						
Woods Excavating[233%]																						

◆ 5/13
 _____ Mair



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

Resource Names	January				February				March				April				May				June				July		
	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E		
Lapointe Drywall, Kelly Bros																											
East Coast Electrical, HVAC Services,																											
Lapointe Drywall																											
NE Painting																											
Landy & Son																											
East Coast Electrical, HVAC Services,																											
Triform, Hascall & Hall																											
Chilton Cabinetmakers																											
Landry & Son Acoustics																											
Material Handling Sales, Decorating																											
Great Falls Construction, Kelly Bros																											
NE Painting																											
Welch Signs																											
All Contractors																											



6,080 SF Renovation


Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

August					September			October			November			December			January			February			March			April	
M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M

Maine Reality Advisors, Great Falls Construction

9/15
 9/16

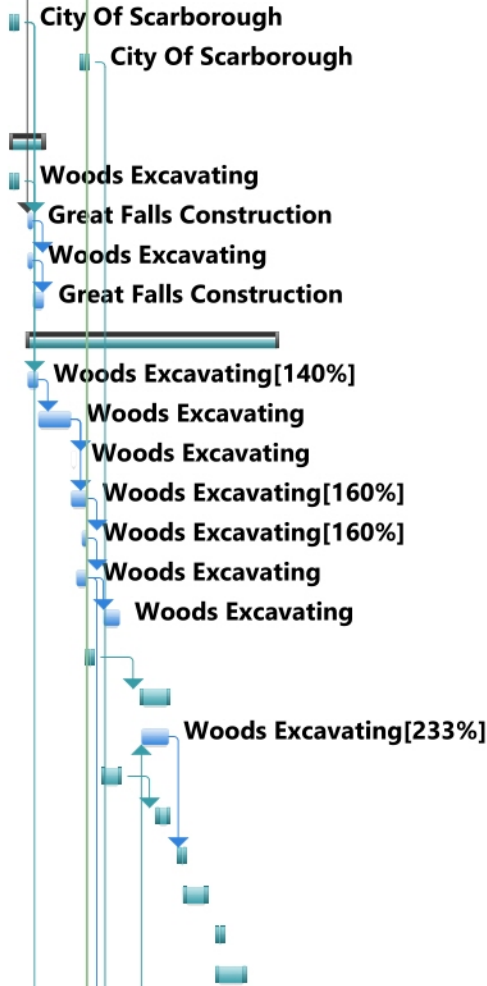




Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

6,080 SF Renovation

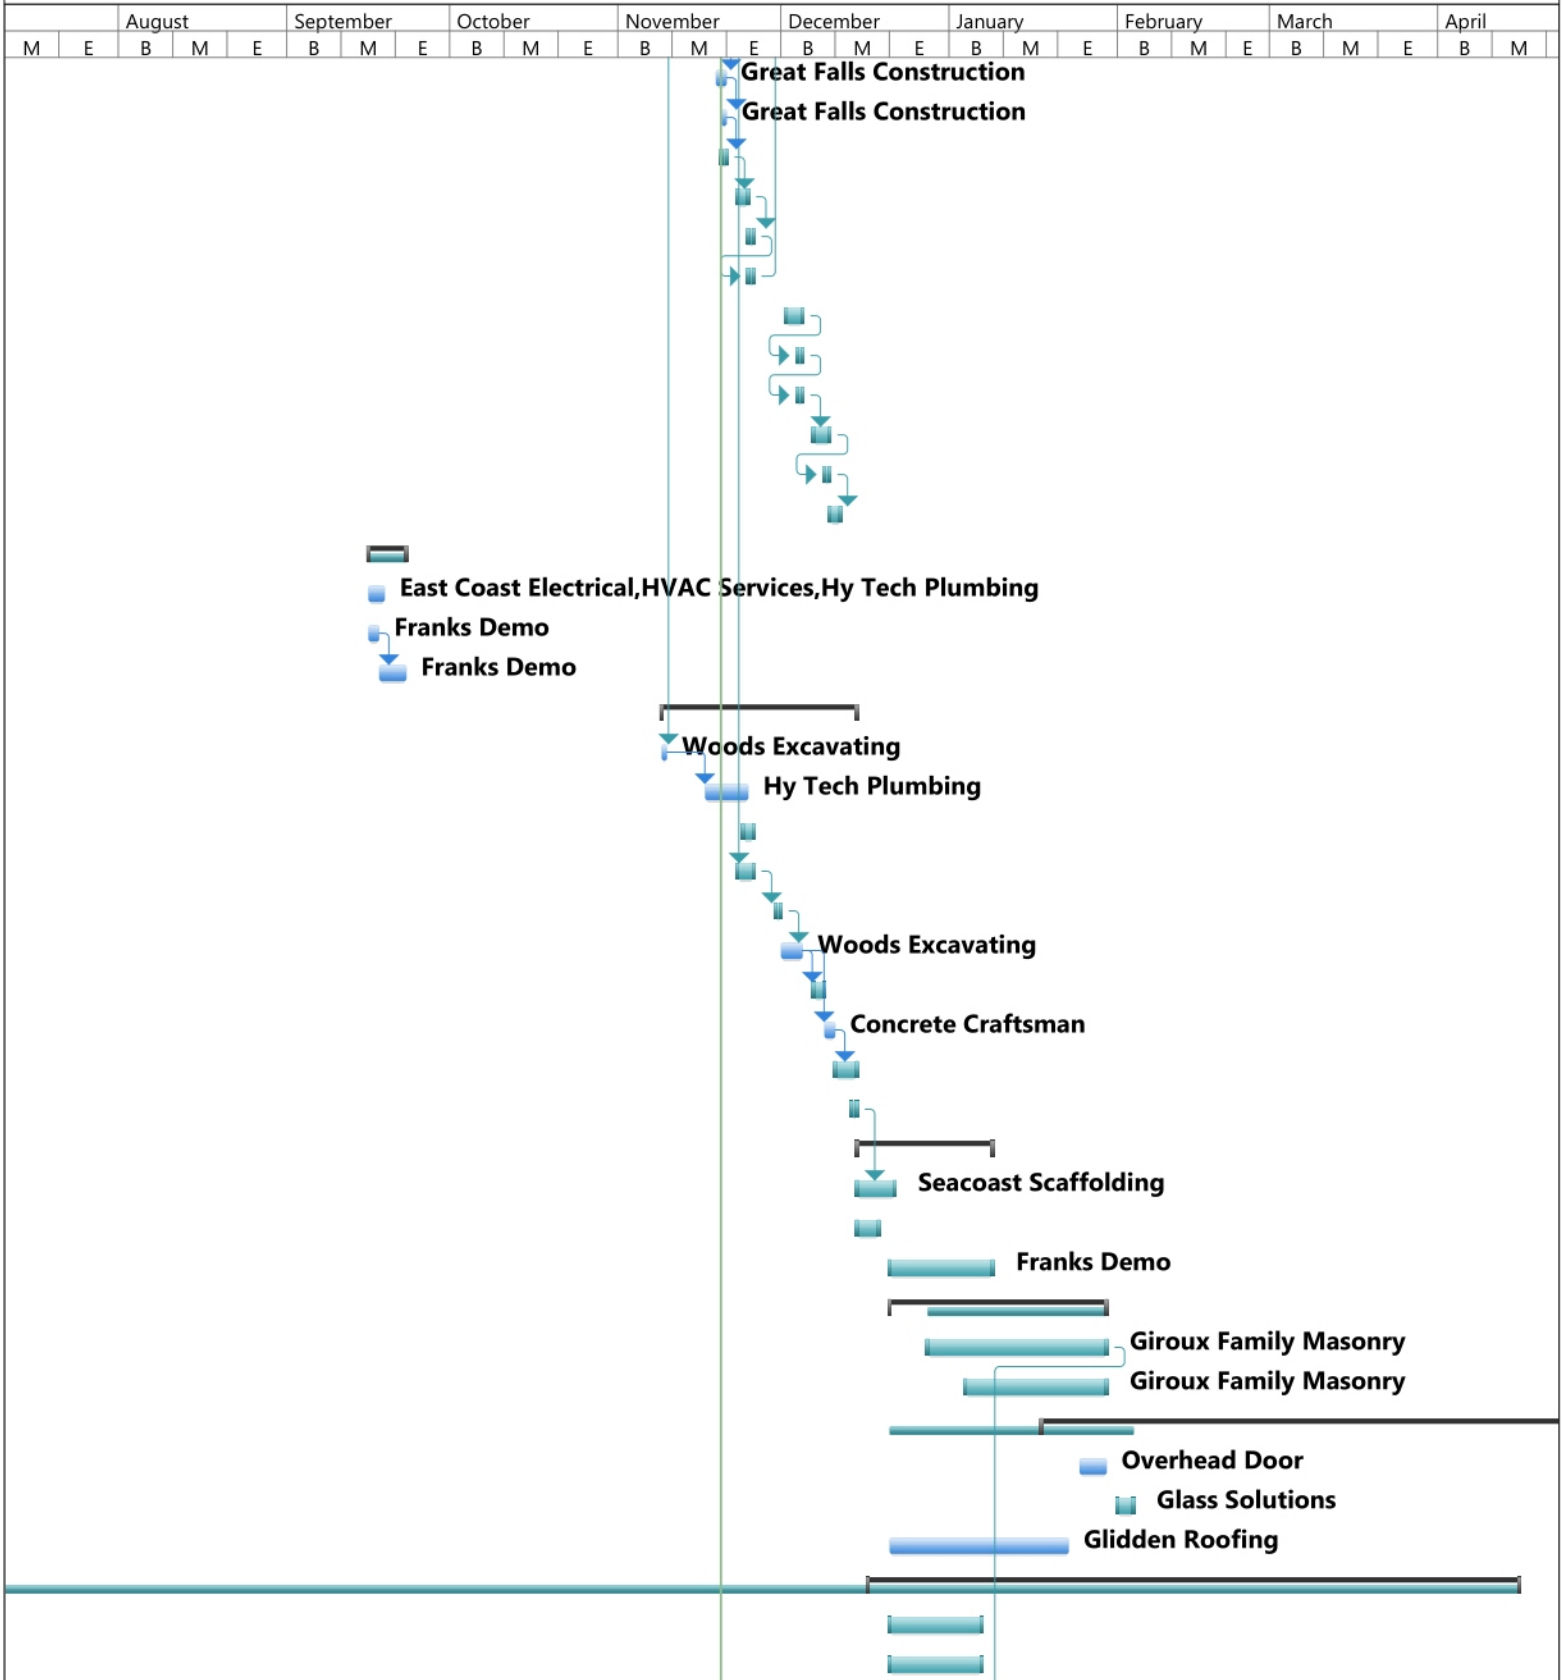




6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

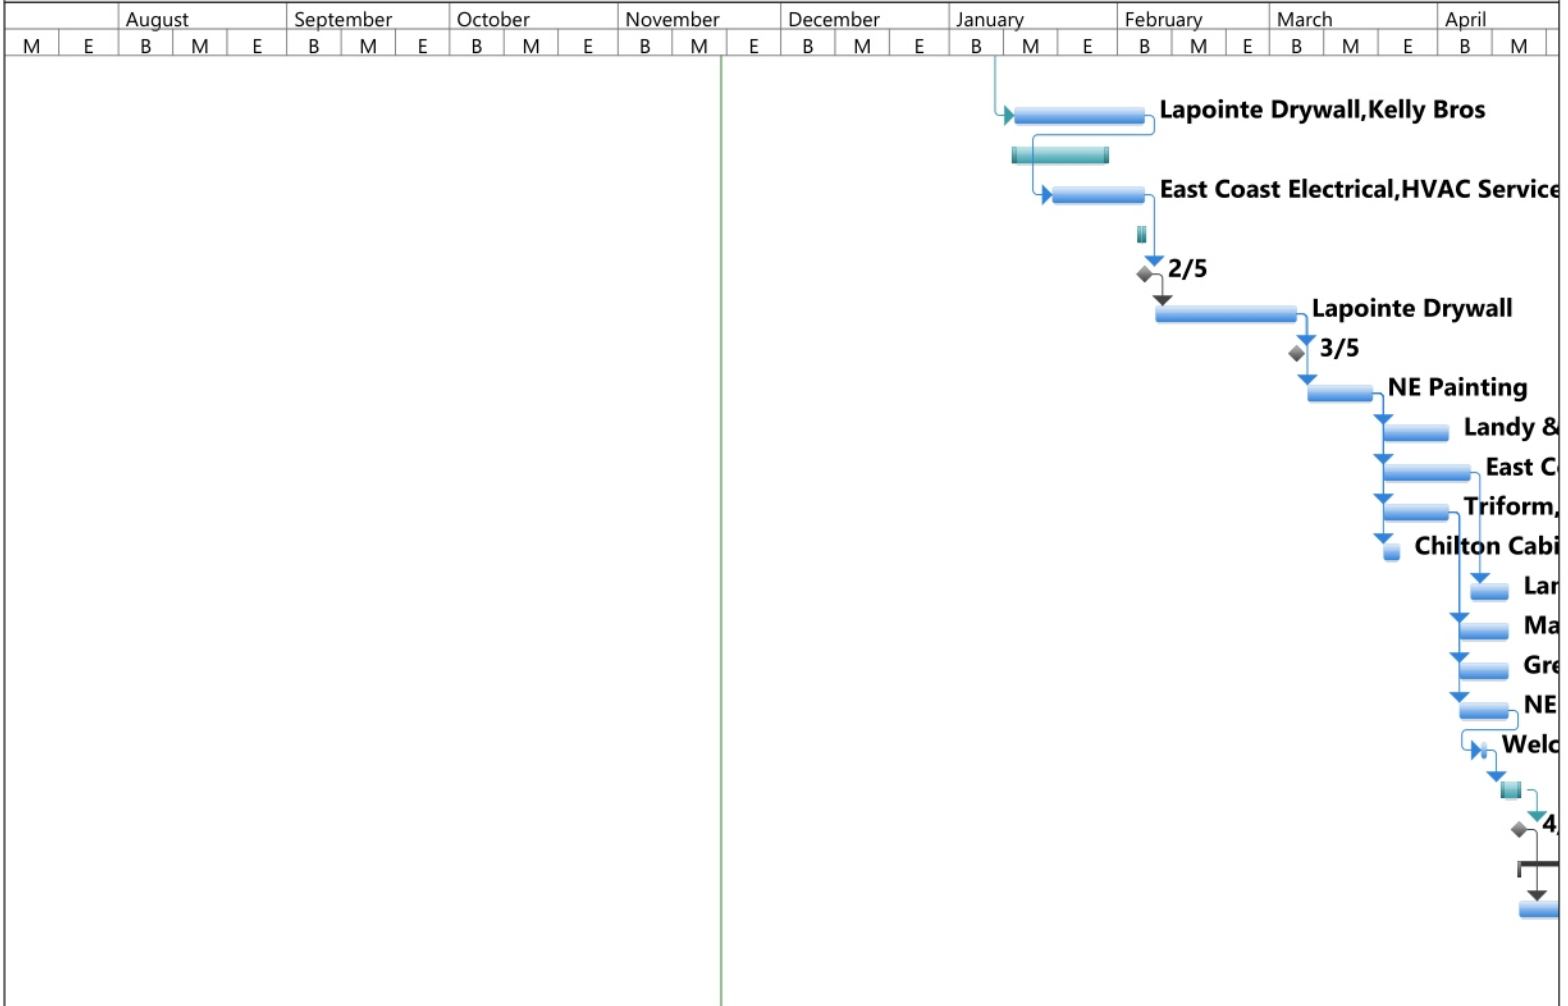



Construction Schedule

40A Manson Libby Road
Scarborough ME 04074
GSA Fitout

6,080 SF Renovation

May				June			July			August			September			October			November			December			January		
E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

May				June			July			August			September			October			November			December			January					
E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--



Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

6,080 SF Renovation

May			June			July			August			September			October			November			December			January					
E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M

ices,Hy Tech Plumbing,Connectivity Point,Minuteman Security

& Son

Coast Electrical,HVAC Services,Hy Tech Plumbing,Connectivity Point,Minuteman Security

m,Hascall & Hall

abinetmakers

andry & Son Acoustics

Material Handling Sales,Decorating Plus,Great Falls Construction,Thompson & Anderson

Great Falls Construction,Kelly Bros

NE Painting

elch Signs

4/15

All Contractors

4/30

From: (b)(6); (b)(7)(C)
Sent: 24 Nov 2020 19:43:50 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda
Importance: High

Finally "Habemus Permit".😊 Happy Thanksgiving to you !!!!!

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, November 24, 2020 2:39 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda

Great news. Thank you.

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

From: (b)(6); (b)(7)(C)
Sent: Tuesday, November 24, 2020 2:28 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE-ERO Scarborough ME - Construction Kickoff Agenda
Importance: High

To all,

From: (b)(6); (b)(7)(C)
Sent: 2 Feb 2021 21:17:51 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson (b)(7)(E)
Importance: High

Thank you (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 2, 2021 4:15 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson (b)(7)(E)

I will look at it tomorrow. I assume sometime after that.

Thank you,

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) [207-780-](tel:207-780-)(b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Tuesday, Feb 02, 2021, 4:13 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Manson (b)(7)(E)

Hi (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thank you,
(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager

O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 27, 2021 4:28 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: 40 Mansor (b)(7)(E)
Importance: High

(b)(6); (b)(7)(C)

(b)(7)(E)

[Redacted content]

Thank you.

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 27, 2021 3:15 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)

Subject: FW: 40 Manson (b)(7)(E)

Importance: High

Hi (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, January 26, 2021 2:40 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: Fwd: 40 Manson (b)(7)(E)

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Good Afternoon (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

----- Forwarded message -----

From: (b)(6); (b)(7)(C)

Date: Tue, Jan 19, 2021 at 1:40 PM

Subject: Fwd: 40 Manson (b)(7)(E)

To: (b)(6); (b)(7)(C)

Cc:

Hi (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thanks,

(b)(6); (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275- (b)(6); (b)(7)(C)

----- Forwarded message -----

From: (b)(6); (b)(7)(C)

Date: Tue, Jan 19, 2021 at 9:22 AM

Subject: 40 Manson (b)(7)(E)

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Hi (b)(6); (b)(7)(C)

(b)(7)(E); (b)(5)

Thanks

(b)(6); (b)(7)(C)

Asst. Project Manager
Great Falls Construction
20 Mechanic Street
Gorham ME 04038
Office: (207) 833- (b)(6); (b)(7)(C)
Cell: (207) 730- (b)(6); (b)(7)(C)

--



U.S. General Services Administration

(b)(6); (b)(7)(C)

Leasing Specialist

Leasing Division

Public Building Service

10 Causeway Street, (b)(6); (b)(7)(C)

Boston, MA 0222

C: (617) 650- (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 2 Feb 2021 21:12:58 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 40 Mansor (b)(7)(E)
Attachments: FW: Letter of Authorization sample form, (b)(7)(E)
Memo.pdf
Importance: High

Hi (b)(6); (b)(7)(C)

(b)(7)(E); (b)(5)

Thank you,
(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 LOAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, January 27, 2021 4:28 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: 40 Mansor (b)(7)(E)
Importance: High

(b)(6); (b)(7)(C)

(b)(7)(E)

(b)(7)(E)

[Redacted]

(b)(6);
(b)(7)(C)

Thank you,

(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-

From: (b)(6); (b)(7)(C)

Sent: Wednesday, January 27, 2021 3:15 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: FW: 40 Manson (b)(7)(E)

Importance: High

Hi (b)(6); (b)(7)(C)

(b)(7)(E); (b)(5)

[Redacted]

(b)(6);
(b)(7)(C)

Thank you,

(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-

From: (b)(6); (b)(7)(C)

Sent: Tuesday, January 26, 2021 2:40 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: Fwd: 40 Manson (b)(7)(E)

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Good Afternoon (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

[Redacted]

From: (b)(6); (b)(7)(C)
Sent: 5 Oct 2016 11:43:49 -0400
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: Letter of Authorization sample form
Attachments: (b)(7)(E)

FYI,
(b)(6); (b)(7)(C) was cc'd on the original email.

Thanks

(b)(6); (b)(7)(C)
(b)(6); (b)(7)(C) Space Management Specialist | Region 4
Office of Asset & Facilities Management
U.S. Department of Homeland Security | Immigration and Customs Enforcement
500 12th Street, SW, (b)(6); (b)(7)(C) Washington, DC 20536
O: (202) 732-(b)(6); (b)(7)(C) | www.ice.gov

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Wednesday, October 05, 2016 11:42 AM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: Letter of Authorization sample form

(b)(5); (b)(6); (b)(7)(C); (b)(7)(E)

Please let me know if you have any questions or concerns. Thanks very much.

(b)(6); (b)(7)(C)
Regional Security Manager, East
Physical Security Operations Unit
Office of Professional Responsibility
U.S. Immigration & Customs Enforcement
777 Gloucester St. (b)(6); (b)(7)(C)
Brunswick, Georgia 31520
Office: (912) 273-(b)(6); (b)(7)(C)
Cell: (912) 577-(b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Wednesday, October 05, 2016 10:37 AM
To: (b)(6); (b)(7)(C)
Cc:

Subject: RE: Letter of Authorization sample form

(b)(6);
(b)(7)(C)

I'm waiting to hear back from the local office.

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) Space Management Specialist | Region 4 Office of Asset & Facilities Management U.S.
Department of Homeland Security | Immigration and Customs Enforcement
500 12th Street, SW (b)(6); (b)(7)(C) Washington, DC 20536
O: (202) 732-(b)(6); (b)(7)(C) | www.ice.gov

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Wednesday, October 05, 2016 7:42 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: Letter of Authorization sample form

(b)(6); (b)(7)(C)

Could you please provide me the name of the HSI representative (b)(7)(E) and their mailing address. (b)(5)

Thanks.

(b)(6); (b)(7)(C)

Regional Security Manager, East
Physical Security Operations Unit
Office of Professional Responsibility
U.S. Immigration & Customs Enforcement
777 Gloucester St. (b)(6); (b)(7)(C)
Brunswick, Georgia 31520
Office: (912) 275-(b)(6);
Cell: (912) 577-(b)(7)(C)

(b)(6); (b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Tuesday, October 04, 2016 3:53 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: FW: Letter of Authorization sample form

Please see attached sample form (b)(7)(E)

(b)(6); (b)(7)(C)

Executive Vice President
Procacci Development Corporation
95 South Federal Highway

(b)(6); (b)(7)(C)

Boca Raton, Florida 33432

tel: 561.416-(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

www.procacci.us

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 30, 2016 3:51 PM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: Letter of Authorization sample form

(b)(6);
(b)(7)(C)

Please see attached sample letter from (b)(6); (b)(7)(C) of Next Door Distribution Company.

Thanks

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C) Space Management Specialist | Region 4 Office of Asset & Facilities Management U.S.

Department of Homeland Security | Immigration and Customs Enforcement

500 12th Street, SW, (b)(6); (b)(7)(C) Washington, DC 20536

O: (202) 732-(b)(6); (b)(7)(C) www.ice.gov

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 30, 2016 7:43 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: Letter of Authorization sample form

Good morning, (b)(7)(E)

See attached sample form.

Thanks

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Friday, September 30, 2016 7:20 AM

To: (b)(6); (b)(7)(C)

Subject: Scanned from a Xerox Multifunction Printer

Please open the attached document. It was scanned and sent to you using a Xerox Multifunction Printer.

Attachment File Type: pdf, Multi-Page

Multifunction Printer Location: machine location not set

Device Name: (b)(6); (b)(7)(C)

For more information on Xerox products and solutions, please visit <http://www.saxon.net>

U.S. Department of Homeland Security
Office of Professional Responsibility
Physical Security Operations - East Region
777 Gloucester Street, Suite 301
Brunswick, GA. 31520



U.S. Immigration and Customs Enforcement

October 5, 2016

(b)(5); (b)(6); (b)(7)(C); (b)(7)(E)

From: (b)(6); (b)(7)(C)
Sent: 2 Feb 2021 13:28:25 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME - Signage Submittal
Importance: High

Good Morning (b)(6); (b)(7)(C)

(b)(5)

Please let me know.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, January 25, 2021 6:54 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME - Signage Submittal

I should be.

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780 (b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Monday, Jan 25, 2021, 5:34 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: ICE Scarborough ME - Signage Submittal

Hi (b)(6); (b)(7)(C)

I hope this email finds you doing well. Could you please go over the room names and the sign's submittal attached? Feel free to edit the names in the excel sheet attached. Let me know if we can review the signs tomorrow morning before our meeting with GSA. Are you available at 10 am tomorrow?

Thank you,

(b)(6), (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6), (b)(7)(C)

Sent: Tuesday, December 22, 2020 4:04 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: ICE Scarborough ME - Signage Submittal

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi

(b)(6), (b)(7)(C)

Please review the attached Signage submittal and provide comments.

Thanks,

(b)(6), (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street (b)(6), (b)(7)(C)
Boston, MA 02222
(C) 617-275 (b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 25 Jan 2021 23:59:52 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME - Signage Submittal
Importance: High

I will send you an invite in Microsoft Teams.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, January 25, 2021 6:54 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME - Signage Submittal

I should be.

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) [207-780-](tel:207-780-)(b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Monday, Jan 25, 2021, 5:34 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: ICE Scarborough ME - Signage Submittal

Hi (b)(6); (b)(7)(C)

I hope this email finds you doing well. Could you please go over the room names and the sign's submittal attached? Feel free to edit the names in the excel sheet attached.

From: (b)(6); (b)(7)(C)
Sent: 2 Mar 2021 14:33:26 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME - Today's Agenda
Importance: High

Thank you all.

Thank you,
(b)(6); (b)(7)(C)
MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Tuesday, March 2, 2021 9:15 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Today's Agenda

I will also be on the call today.

(b)(6); (b)(7)(C)
MPA, HQERO Facilities Support Unit
Operations Support Division
Enforcement and Removals Operations
U.S. Immigration and Customs Enforcement Headquarters
500 12th Street, S.W. Washington, D.C. 20536
Desk: 202.732-(b)(6); (b)(7)(C)
Be the Change You Want to See in the World~ *Gandhi

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Tuesday, March 2, 2021 9:05 AM
To: (b)(6); (b)(7)(C)
Cc:
Subject: ICE Scarborough ME - Today's Agenda
Importance: High

(b)(6); (b)(7)(C)

Sorry, I am not going to be able to join the meeting. Could you please assist me with the meeting today? FYI, I do not have any pending submittals. I have forwarded all of them to (b)(6); (b)(7)(C) GSA has to respond about Miscellaneous Plumbing and Turf submittals.

You can text me at my cell for any questions or concerns during the meeting.

Thank you in advance for your cooperation.

(b)(6), (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | QAFM Project Manager
O: 305-597-
C: 202-754-

(b)(6),
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 19 Nov 2020 13:27:49 +0000
To: (b)(6); (b)(7)(C)
Subject: RE: Movement of ICE Inmates
Attachments: FW: Movement of ICE Inmates

(b)(6);
(b)(7)(C)

The Sheriff also advised, in the second email, that per state order, all people entering Maine, other than from NH or VT, must be quarantined for 14 days, unless proof of COVID test. This includes detainees. This would eliminate any out of state transfers to CCJ, other than from MAN or STA. Even field arrest wise.

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

From: (b)(6); (b)(7)(C)
Sent: Thursday, November 19, 2020 8:17 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: FW: Movement of ICE Inmates

Heads up

From: (b)(6); (b)(7)(C)
Date: Thursday, Nov 19, 2020, 7:47 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: FW: Movement of ICE Inmates

Good morning,

I am sure most of you use Cumberland County Jail (CCJ) for inmates released to CAP. Unfortunately the CCJ has informed ICE that they will no longer accept ICE detainees when being transferred from another facility until the attached procedures are followed. This change does not affect at-large arrest. (A)AFOD Wesling and his team are working on a solution and will provide updated guidance in the near future. For all CAP release, not mandatory detention, will be placed on ATD. Please continue to work with (A)SDDO (b)(6); (b)(7)(C) or detention space.

This is a fluid situation so please be patient.

(b)(6); (b)(7)(C)

Assistant Field Office Director/Enforcement
Boston Field Office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
202-774-^{(b)(6);}
_{(b)(7)(C)}

From: (b)(6); (b)(7)(C)
Sent: Thursday, November 19, 2020 7:15 AM
To: (b)(6); (b)(7)(C)
Subject: FW: Movement of ICE Inmates

For your awareness. I'll be working with my staff today to come up with possible solutions, but as of now Cumberland County will not accept cases coming out of another facility. This essentially shuts down CAP intakes for us as they were the only reliable spot. I will keep you posted, but expect that non-mandatory detention CAP releases will have to be put on ATD for the interim.

(b)(6); (b)(7)(C)

(A)AFOD, Custody Management
Boston Field Office

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Wednesday, Nov 18, 2020, 18:47
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: Movement of ICE Inmates

All,

Please see below, and attached. Effective immediately per Sheriff Joyce.

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-^{(b)(6);}
_{(b)(7)(C)}

176 Gannett Drive
South Portland, ME 04106

From: Kevin Joyce (b)(6); (b)(7)(C)
Sent: Wednesday, November 18, 2020 3:44 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: Movement of ICE Inmates

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Good afternoon (b)(6); (b)(7)(C)

As you know on Friday November 13, 2020, the Bristol County Sheriff's Office arrived at our facility at approximately 19:00 hours with three ICE inmates.

Our staff followed our long standing protocol of testing ALL inmates in the vehicle prior to entering the Cumberland County Jail. Consequently, one of the inmates tested positive for COVID-19. Given that some, if not all of the inmates had been transported from a holding facility and were in close contact with each other for 2 hours plus, it was safe to assume that given we had one positive COVID test and it is likely the two others who were exposed for a long period of time would have tested positive after a period of incubation. Their entrance was ultimately refused.

Our staff has been very aggressive in accommodating various law enforcement agencies, but the movement of inmates is extremely concerning and very risky to our staff and our inmate population

The short notice of transfers of any inmate, ICE inmates, Federal inmates or other County Jail inmates were pretty benign prior to COVID-19, but give the current circumstance and the increasing number of COVID cases popping up, we are forced to set a new process for accepting ICE inmates from an interfacility transfer.

Effective immediately, the process for inmate transfer will be enforced.

(b)(6); (b)(7)(C)
This does not affect any arrests coming from the "field".

It appears that an individual by the name of (b)(6); (b)(7)(C) is scheduling these transfers. I have not been able to obtain an email address for (b)(6); (b)(7)(C)

Would you please make sure that the attached document gets relayed accordingly?

Thanks,

--

Kevin J. Joyce, MBA, CHPP, CCE
Sheriff
Sheriff's Office Law Enforcement

(b)(6);
(b)(7)(C)

Cumberland County
774 
FBINA 218th Session



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.

From: (b)(6); (b)(7)(C)
Sent: 19 Nov 2020 01:49:13 +0000
To: (b)(6); (b)(7)(C)
Subject: FW: Movement of ICE Inmates

fyi

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

From: Kevin Joyce (b)(6); (b)(7)(C)
Sent: Wednesday, November 18, 2020 7:27 PM
To: (b)(6); (b)(7)(C)
Subject: Re: Movement of ICE Inmates

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Good evening (b)(6); (b)(7)(C)

All of the inmate transfers in Maine are pre-planned before the transfer is done. Even before COVID inmate transfers were planned as a courtesy to the receiving agency. Earlier this year, due to COVID especially early on, we did not transfer inmates. In essence we don't transfer individuals unless absolutely necessary.

Currently any citizen who is coming into Maine from any state other than VT and NH must quarantine for 14 days or show a positive test to enter Maine. Why wouldn't this work for inmates? Additionally, we are not doing out of state extraditions unless absolutely necessary due to COVID. It is not worth the risk to our staff.

As of late we have been getting 3-4 hour notification of an ICE inmate transfer??? That might be acceptable under "normal" circumstances, but not now. There is no urgency on inmate transfers.

The bottom line is that in Maine, we have been conscientious in being extremely careful and aggressive in preventing virus transmission between facilities. I won't get into the state transfers as we are extremely limited and controlled by how and when we transfer inmates. I will not get as restrictive as the state, but I must protect my staff and facility. The continual movement of inmates into our facility from out of state is a HUGE risk for the jail. Unless we (collectively) do everything we can to prevent an outbreak, it will happen.

I don't believe inmate transfer unless ABSOLUTELY necessary is a wise decision for either of us.

As for arrests in the field, we will accept inmates just like I accept every other law enforcement arrest. Including inmates that test positive.

Hopefully this helps.

On Wed, Nov 18, 2020 at 6:54 PM (b)(6); (b)(7)(C) wrote:

Good evening

I sent your directive to ICE Boston.

I am concerned about arrests locally here in Maine from the State prisons and county jails. Do you know if they are able to meet these standards? Is my office okay if taking detainees from within Maine county jails and prisons?

(b)(6); (b)(7)(C)

Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780- (b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

From: Kevin Joyce (b)(6); (b)(7)(C)
Sent: Wednesday, November 18, 2020 3:44 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: Movement of ICE Inmates

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Good afternoon

As you know on Friday November 13, 2020, the Bristol County Sheriff's Office arrived at our facility at approximately 19:00 hours with three ICE inmates.

Our staff followed our long standing protocol of testing ALL inmates in the vehicle prior to entering the Cumberland County Jail. Consequently, one of the inmates tested positive for COVID-19. Given that some, if not all of the inmates had been transported from a holding facility and were in close contact with each other for 2 hours plus, it was safe to assume that given we had one positive COVID test and it is likely the two others who were exposed for a long period of time would have tested positive after a period of incubation. Their entrance was ultimately refused.

From: (b)(6); (b)(7)(C)
Sent: 29 Mar 2021 13:04:55 +0000
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: (b)(6); (b)(7)(C)
Importance: High

(b)(6); (b)(7)(C) and all,

Please contact (b)(6); (b)(7)(C) to add all the things you need to move or dispose of. All this information (equipment, boxes needed per employee, individual printers, scanners, etc.) shall be specified in the Excel sheet I sent to (b)(6); (b)(7)(C) so GSA can give me a cost estimation to move.

The field office needs to coordinate the information of the Excel list, and provide it to us asap.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, March 29, 2021 8:44 AM
To: (b)(6); (b)(7)(C)
Subject: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Regards,

(b)(6); (b)(7)(C)
IT Specialist
New England Area
East Region | IT Field Operations Branch
IT Operations Division | OCIO
U.S. Immigration and Customs Enforcement | DHS



Office: 207-808-(b)(6); (b)(7)(C)

Mobile: 207-809-(b)(6);
(b)(7)(C)

Email: (b)(6); (b)(7)(C)

**ICE Service Desk: 888-347-(b)(6);
(b)(7)(C)** or via web (b)(7)(E)

(b)(7)(E)



(b)(7)(E)



From: (b)(6); (b)(7)(C)
Sent: 30 Sep 2020 18:55:23 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO Scarborough, ME - Questions regarding ICE for VA (co-locating in same building)
Importance: High

Thank you (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, September 30, 2020 2:44 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO Scarborough, ME - Questions regarding ICE for VA (co-locating in same building)

There have not been any protestors at 176 Gannett Drive.

155 Gannett is CBP.

(b)(6); (b)(7)(C)
SDDO
ICE ERO Portland, ME Sub-Office
[176 Gannett Drive](#)
[South Portland, ME 04106](#)

Main Office Phone#: 207-780 (b)(6); (b)(7)(C)
Desk Phone#: 207-808 (b)(6); (b)(7)(C)
Cell Phone#: 207-252 (b)(7)(C)
Fax#: [207-780-3216](#)

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)

Date: Wednesday, Sep 30, 2020, 2:41 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: ERO Scarborough, ME - Questions regarding ICE for VA (co-locating in same building)

Good afternoon

(b)(6); (b)(7)(C)

I am reaching out to see if you can provide any general information about the frequency and size of protests you've experience at Gannett Drive over the past year or so. Please let me know.

(b)(5)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-
C: 202-754-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 25 Mar 2021 17:17:49 +0000
To: (b)(6); (b)(7)(C)
Subject: RE: ERO Scarborough Moving and Installation meeting
Importance: High

I am so glad to hear that. Thank you much for letting me know. Take care.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, March 25, 2021 12:58 PM
To: (b)(6); (b)(7)(C)
Subject: RE: ERO Scarborough Moving and Installation meeting

(b)(6);
(b)(7)(C)

Hi (b)(6); (b)(7)(C) We were just over at the job site with (b)(6); (b)(7)(C) It's looking great.

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Thursday, Mar 25, 2021, 12:34 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ERO Scarborough Moving and Installation meeting

Attached please find updated schedule.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, March 11, 2021 10:43 AM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ERO Scarborough Moving and Installation meeting
Importance: High

Thank you for your feedback. Please disregard the previous draft schedule. Attached updated schedule.

(b)(6); (b)(7)(C); (b)(5); (b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

-----Original Message-----

From: (b)(6); (b)(7)(C)

Sent: Thursday, March 11, 2021 9:02 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: ERO Scarborough Moving and Installation meeting
Importance: High

Attached updated schedule for our meeting.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
(b)(7)(C)

C: 202-754

(b)(6);
(b)(7)(C)

ERO Scarborough	
Moving coordination and installation-03-25-21	
Furniture measurement	Monday, April 12, 2021
GC's Electrician - furniture boxes will be delivered	Monday, April 12, 2021
Substantial Completion date	Friday, May 14, 2021
Pots lines installation	Monday, May 17, 2021
Furniture Installation begins	Monday, May 24, 2021
Furniture punch walk through	Friday, May 28, 2021
Occupancy & Turnover	Friday, June 4, 2021
Activate Alarm System at Scarborough	Friday, June 4, 2021
OCIO disconnecting at 176 Gannett Drive	Friday, June 4, 2021
Moving Date after disconnecting	Friday, June 4, 2021
System installation begins / Scarborough	Friday, June 4, 2021
Final installation & connectivity	Monday, June 7, 2021

From: (b)(6); (b)(7)(C)
Sent: 25 Mar 2021 13:04:59 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO-HSI Warwick 100% Final CDs drawings Email 2 of 2 MEP
Importance: High

(b)(6);
(b)(7)(C)

My apologies (b)(6); (b)(7)(C) I used Warwick's email to confirm with (b)(6) the inspection today at Scarborough. Please disregard the Warwick email.

Thank you.

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, March 25, 2021 8:48 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: ERO-HSI Warwick 100% Final CDs drawings Email 2 of 2 MEP

This says Warwick. Do you mean Scarborough?

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)
176 Gannett Drive
South Portland, ME 04106

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Thursday, Mar 25, 2021, 8:46 AM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO-HSI Warwick 100% Final CDs drawings Email 2 of 2 MEP

(b)(5); (b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, March 25, 2021 8:41 AM

To: (b)(6); (b)(7)(C)

Subject: RE: ERO-HSI Warwick 100% Final CDs drawings Email 2 of 2 MEP

(b)(5); (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, March 22, 2021 12:00 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ERO-HSI Warwick 100% Final CDs drawings Email 2 of 2 MEP

Importance: High

Email 2 of 2 MEP.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: [REDACTED]
Sent: Monday, March 22, 2021 11:49 AM
To: [REDACTED]

Subject: ERO-HSI Warwick 100% Final CDs drawings Email 1 of 2 Architecture.
Importance: High

To all reviewers,

Attached please find ERO-HSI Warwick 100% Final CDs drawings for your review and comments. Email 1 of 2 Architecture.

We need your final review and comments on, or before **Friday 26, 2020**.

I will send another emails for the remainder of the full CDs.

Please let me know if you need any other additional information.

Thank you,

[REDACTED]
MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
HSI SAC Miami
11226NW 20th Street
Miami, FL 33172
O:305-597-[REDACTED]
C: 202-754-[REDACTED]

From: (b)(6); (b)(7)(C)
Sent: 30 Nov 2020 23:50:00 +0000
To: (b)(6); (b)(7)(C)
Subject: RE: Fwd: Three to Cumberland. Two Field arrests and one Pre-approved facility transfer.

(b)(5)

Have a good night.

(b)(6); (b)(7)(C)
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-(b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Monday, Nov 30, 2020, 6:37 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: Fwd: Three to Cumberland. Two Field arrests and one Pre-approved facility transfer.

Thanks (b)(6); (b)(7)(C) we're working on alternate arrangements for the 3. Just FYI in case it comes up, this individual was quarantined in the MA DOC per CCJ's recent guidelines. A PCR test was conducted while he was in quarantine and he was negative, which is much more reliable than the rapid tests being done in the sally port. He was cleared and accepted by CCJ in accordance with their guidelines for accepting CAP releases.

(b)(6); (b)(7)(C)
(A)Assistant Field Office Director, Custody Management
Boston Field Office

Enforcement and Removal Operations
U.S. Immigration And Customs Enforcement
Cell 617-799-[REDACTED]

From: [REDACTED]
Sent: Monday, November 30, 2020 6:30 PM
To: [REDACTED]
[REDACTED]
Subject: FW: Fwd: Three to Cumberland. Two Field arrests and one Pre-approved facility transfer.

Fyi

[REDACTED]
Supervisory Detention & Deportation Officer
Boston Field Office, Portland, ME Sub-office
Enforcement and Removal Operations
U.S. Immigration and Customs Enforcement
(Office) 207-780-[REDACTED]

Sent with BlackBerry Work
(www.blackberry.com)

From: [REDACTED]
Date: Monday, Nov 30, 2020, 6:22 PM
To: [REDACTED]
Subject: Fwd: Three to Cumberland. Two Field arrests and one Pre-approved facility transfer.

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

[REDACTED]
[REDACTED]

I received a call on my way home a short time ago, the three ICE Inmates listed below arrived with Bristol County. During the COVID screening process, [REDACTED] aka; [REDACTED] tested COVID positive.

I spoke with Sheriff Joyce and the decision was to refuse all three ICE detainees, due to positive test and due to the close conduct with a known positive (the other two).

I'm at home currently, so if you need more information, you will need to call me, 329-[REDACTED]

Thanks,

(b)(6); (b)(7)(C)

Captain-Corrections
Cumberland County Sheriff's Office
50 County Way
Portland, Maine 04102
Direct: 207-245-
(b)(6);
(b)(7)(C)

Capt,

Here is the needed information:

The staff that went out to test the individuals was Officer (b)(6); (b)(7)(C) and RN (b)(6); (b)(7)(C). They both were wearing all appropriate PPE and had no exposure.

The names of the Deputies from Bristol County are as follows:

(b)(6); (b)(7)(C)

They are headed to Burlington from here.

The individual that tested Positive was (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6);
(b)(7)(C)

----- Forwarded message -----

From: (b)(6); (b)(7)(C)

Date: Mon, Nov 30, 2020 at 2:23 PM

Subject: Three to Cumberland. Two Field arrests and one Pre-approved facility transfer.

To: (b)(6); (b)(7)(C)

Cc:

Good afternoon,

Two field arrests along with one pre-approved facility transfer will be transported to Cumberland County Jail this afternoon. Rough ETA 1700hrs.

(b)(6); (b)(7)(C)

DOB: (b)(6); (b)(7)(C)

COC: Guatemala

Gangs: none found.

Classification: Med/High.

Temp is 97.5 at 1210hrs
Subject shows no signs/symptoms of COVID and claimed to be in good health.

(b)(6), (b)(7)(C)

DOB: (b)(6), (b)(7)(C)

COC: Guatemala

Classification: Med/High

Temp is 97.3 at 0937hrs

Subject shows no signs/symptoms of COVID and claimed to be in good health

PRE APPROVED FACILITY TRANSFER BY SGT (b)(6), (b)(7)(C)

(b)(6), (b)(7)(C)

DOB (b)(6), (b)(7)(C)

COC: Dominican Republic

Classification: High

Temp is 97.5 at 1100hrs

Subject shows no signs/symptoms of COVID. Subject claimed to be in good health.

Thank you,

(b)(6), (b)(7)(C)

(A)SDDO/Intake/processing/bonds/property

Boston Field Office

Enforcement and Removal Operations

Immigration & Customs Enforcement

781-853

(b)(6);
(b)(7)(C)

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO) Law Enforcement Sensitive. It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

--
(b)(6), (b)(7)(C)

Sergeant Intake/Booking

Sheriff's Office

Cumberland County

774

(b)(6);
(b)(7)(C)



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as

public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.



Notice: Under Maine law, documents - including e-mails - in the possession of public officials or employees about government business may be classified as public records. There are very few exceptions. As a result, please be advised that what is written in an e-mail could be released to the public and/or the media if requested.

From: (b)(6); (b)(7)(C)
Sent: 8 Mar 2021 16:56:54 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: GSA DHS Scarborough Signage Submittal
Importance: High

(b)(6);
(b)(7)(C)

(b)(7)(E)

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, March 8, 2021 11:54 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: GSA DHS Scarborough Signage Submittal

Hi All,

(b)(5)



U.S. Immigration
and Customs
Enforcement

(b)(5)

(b)(6); (b)(7)(C)

MPA, HQERO Facilities Support Unit
Operations Support Division

**Enforcement and Removals Operations
U.S. Immigration and Customs Enforcement Headquarters
500 12th Street, S.W. Washington, D.C. 20536**

Desk: 202.732 (b)(6); (b)(7)(C)

Be the Change You Want to See in the World~

***Gandhi**

From: (b)(6); (b)(7)(C)

Sent: Monday, March 8, 2021 11:24 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: FW: GSA DHS Scarborough Signage Submittal

(b)(6); (b)(7)(C)

Attached the impact wall signage Lobby and Conference room for your new location. They look good to me, but I would like your approval.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, March 8, 2021 11:18 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: GSA DHS Scarborough Signage Submittal

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

(b)(6); (b)(7)(C)

Please see the attached revised submittal for the impact wall signage for the 40 Manson Libby project. Please let me know if you have any additional comments so I can get this returned to the contractor ASAP.

Thank you

(b)(6); (b)(7)(C) AIA, NCARB

ARCHITECT, PROJECT MANAGER, FIRM ASSOCIATE

Maine Licensed Architect



207.828 (b)(6);
207.659 (b)(7)(C)

30 Danforth Street

(b)(6); (b)(7)(C)

Portland, ME 04101

wbrcae.com | [Facebook](#) | [LinkedIn](#) | [Twitter](#)

From: (b)(6); (b)(7)(C)
Sent: 11 Feb 2021 15:29:48 +0000
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Executed Lease
Importance: High

Thank you!

From: (b)(6); (b)(7)(C)
Sent: Thursday, February 11, 2021 9:45 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Executed Lease

Just a heads up, I sent those questions to (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Sent with BlackBerry Work
(www.blackberry.com)

From: (b)(6); (b)(7)(C)
Date: Thursday, Feb 11, 2021, 9:21 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: ICE Scarborough ME - Executed Lease

(b)(6); (b)(7)(C)

Attached is a copy of the executed lease for your records.
Please let me know if you need any other additional information.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6); (b)(7)(C)
C: 202-754-(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 19 Jan 2021 17:40:37 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 1.19.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda-15.docx
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you.

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 29, 2020 12:00 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda and schedule for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 15, 2020 1:08 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: FW: ICE Scarborough ME - 12.11.20 Meeting Agenda

FYI, see attached agenda for today's meeting.

Thank you,

(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 15, 2020 11:53 AM
To: (b)(6); (b)(7)(C)
Cc: [Redacted]
Subject: ICE Scarborough ME - 12.11.20 Meeting Agenda

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

Attached is the meeting agenda for today's meeting.

Thanks,

(b)(6); (b)(7)(C)
Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275-[Redacted]

(b)(6);
(b)(7)(C)



Meeting Agenda

Job: ICE Building – Fitout
Location: 40 Manson Libby Road - (b)(6); (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340.(b)(6); (b)(7)(C)

Date: 1/19/2021
Meeting: 15

Attendees

(b)(6); (b)(7)(C)

Item Description

Regular Business

- 0.1 Current Work & Quality –Discuss upcoming inspections and non-conforming work if any**
We have demoed the walls on the east side of the building. The masons have started to install the CMU exterior walls. We have begun the demo on the north wall.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
For the next few weeks it will be demolition and CMU erection.
- 0.3 RFI’s – Review log and discuss potential for new items**
RFI 036 - Ballistic Mat
RFI 039 - Shower Floors
RFI 040 - Window Location
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 01_Appendix A_Security_001 – GFC requests this to be expedited
 - 088000_Interior Window Film_003
 - 102113_Toilet Compartments_001
 - 220000_Oil Water Seperator_001
 - 329200_Turf_001
 - Appenidx E_Building Signage_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Future Change Orders
 - RFC No 12 - January Winter Conditions
 - RFC 13 - Demising Wall CL 4 – two options sent 1/7



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

0.6 ASI/SKs – Review potential changes to the contract documents

None

0.7 Payment Application – Review pencil requisition, submission, and payment status

Req 5 will be sent the first week in February. WBRC and GFC will have an onsite review meeting to review the req the second week in February.

Old Business

New Business

15.1 (b)(7)(E)



15.2 (b)(7)(E)



Please notify (b)(6), (b)(7)(C) of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 26 Jan 2021 17:55:08 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 1.26.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda-16.docx
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, January 19, 2021 12:41 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 29, 2020 12:00 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda and schedule for our meeting today.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 15, 2020 1:08 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ICE Scarborough ME - 12.11.20 Meeting Agenda

FYI, see attached agenda for today's meeting.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 15, 2020 11:53 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: ICE Scarborough ME - 12.11.20 Meeting Agenda

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

Attached is the meeting agenda for today's meeting.

Thanks,

(b)(6); (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275-(b)(6); (b)(7)(C)

(b)(6);
(b)(7)(C)



Meeting Agenda

Job: ICE Building – Fitout
Location: 40 Manson Libby Road (b)(6); (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340 (b)(6); (b)(7)(C)

Date: 1/25/2021
Meeting: 16

Attendees

(b)(6); (b)(7)(C)

Item	Description
------	-------------

Regular Business

- 0.1 Current Work & Quality –Discuss upcoming inspections and non-conforming work if any**
The south wall installation is complete. The demolition of the east wall is complete and the installation of the new wall near complete. The north wall demolition has begun.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
For the next week we will continue to construction the exterior walls and begin on the interior CMU walls.
- 0.3 RFI’s – Review log and discuss potential for new items**
RFI 039 - Shower Floors
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 102113_Toilet Compartments_001
 - 220000_Oil Water Seperator_001
 - 329200_Turf_001
 - 220500_Misc Plumbing_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Future Change Orders
 - RFC No 12 - January Winter Conditions
 - RFC 13 - Demising Wall CL 4 – two options sent 1/7
 - RFC No 14 - Window Detail – sent 1/22
- 0.6 ASI/SKs – Review potential changes to the contract documents**
None



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

0.7 Payment Application – Review pencil requisition, submission, and payment status

Req 5 will be sent the first week in February. WBRC and GFC will have an onsite review meeting to review the req the second week in February.

Old Business

15.1 (b)(5), (b)(7)(E)



New Business

16.1 XX
1.25.2021 –

Please notify (b)(6), (b)(7)(C) of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 2 Feb 2021 18:12:27 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 2.2.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda-17.docx
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, January 26, 2021 12:55 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, January 19, 2021 12:41 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 29, 2020 12:00 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Meeting Agenda

Importance: High

Attached please find meeting agenda and schedule for our meeting today.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 15, 2020 1:08 PM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ICE Scarborough ME - 12.11.20 Meeting Agenda

FYI, see attached agenda for today's meeting.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 15, 2020 11:53 AM

To: (b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

Subject: ICE Scarborough ME - 12.11.20 Meeting Agenda

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

Attached is the meeting agenda for today's meeting.

Thanks,

(b)(6); (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275 (b)(6); (b)(7)(C)



Meeting Agenda

Job: ICE Building – Fitout
Location: 40 Manson Libby Road - (b)(6); (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340 (b)(6); (b)(7)(C)

Date: 2/2/2021
Meeting: 17

Attendees

(b)(6); (b)(7)(C)

Item Description

Regular Business

- 0.1 Current Work & Quality –Discuss upcoming inspections and non-conforming work if any**
The east wall installation is complete. The demolition of the north wall is complete and the installation of the new wall in process. Began work on interior masonry walls at Holding Rooms.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
For the next week we will continue to construction the exterior walls and begin on the interior CMU walls. We are working on the layout and coordination of all items withing the interior CMU walls.
- 0.3 RFI’s – Review log and discuss potential for new items**
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 078413_Firestopping_001
 - 102113_Toilet Compartments_001
 - 220000_Oil Water Seperator_001
 - 329200_Turf_001
 - 220500_Misc Plumbing_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Future Change Orders
 - RFC No 12 - January Winter Conditions – GFC is compiling the last T&M Slips & will send by tomorrow.
 - RFC 13 - Demising Wall CL 4 – GFC to revise with new UL rated wall and send today
 - RFC No 14 - Window Detail – GFC to review pricing and revise by tomorrow



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

0.6 ASI/SKs – Review potential changes to the contract documents
None

0.7 Payment Application – Review pencil requisition, submission, and payment status
Req 5 will be sent by Thursday this week. WBRC and GFC will have an onsite review meeting on Tuesday 2/9.

Old Business

15.1 (b)(5); (b)(7)(E)

New Business

17.1 Door 120
2.2.2021 – Please provide preference for active leaf. We suggest left panel closest to Card Reader.

17.2 Soap Dish
2.2.2021 – Need the Mounting height for soap dish in holding cell as it is not integral with the toilet fixture. We assume above and centered on sink.

17.3 Door Hardware
2.2.2021 – Has GSA had an opportunity to review the door hardware questions sent last week after the call?

Please notify (b)(6); (b)(7)(C) of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 16 Feb 2021 14:53:20 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 2.16.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda-19.pdf
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAEM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 2, 2021 1:12 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAEM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, January 26, 2021 12:55 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, January 19, 2021 12:41 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you.

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 29, 2020 12:00 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda and schedule for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 15, 2020 1:08 PM
To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: FW: ICE Scarborough ME - 12.11.20 Meeting Agenda

FYI, see attached agenda for today's meeting.

Thank you.

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Tuesday, December 15, 2020 11:53 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: ICE Scarborough ME - 12.11.20 Meeting Agenda

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi

(b)(6); (b)(7)(C)

Attached is the meeting agenda for today's meeting.

Thanks,

(b)(6); (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275 (b)(6);
(b)(7)(C)



Meeting Agenda

(b)(6);
(b)(7)(C)

Job: ICE Building – Fitout
Location: 40 Manson Libby Road - [redacted] Scarborough ME 04074
Meeting #: Teleconference – 505.340.[redacted]

Date: 2/16/2021
Meeting: 19

Attendees

[redacted]

Item	Description
------	-------------

Regular Business

- 0.1 Current Work & Quality – Discuss upcoming inspections and non-conforming work if any**
[redacted] All rough in pathways have been installed in these walls.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
The masons will continue the interior CMU walls in the sally port and processing. The drywall materials will be delivered. Plumbing, HVAC and electrical rough in will begin. We will begin on the demising wall to the tenant space.
- 0.3 RFI's – Review log and discuss potential for new items**
RFI 043 - Landscaping
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 078413_Firestopping_001
 - 102113_Toilet Compartments_001
 - 220500_Misc Plumbing_001
 - 329200_Turf_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Future Change Orders
 - RFC 15 – February Winter Conditions
- 0.6 ASI/SKs – Review potential changes to the contract documents**
None
- 0.7 Payment Application – Review pencil requisition, submission, and payment status**



Old Business

18.1 Holding Cell Light Switches

2.9.2021 – Please provide a location for the light switches at Holding Room Doors 113, 114 and 115. Plans show the switches in the metal door frames and provisions were not made for that. Mechanical plan also shows a T-stat in the same location on Door #114. We propose moving the light switches to the CMU walls which separate the cells and to relocate the T-stat to one of the same CMU walls. If that is acceptable, Will need to provide height for T-stat as it cannot be located at 48” because the switch will be in the way.

18.2 (b)(5); (b)(7)(E)




18.3 Mop Sink

2.9.2021 – Please clarify US-1. Is it a mop sink that sits on the floor or does it sit on legs. Provide detail or dimensions for location of Eyewash handle. Refer to previous email dated 1-5-2021 with spec and submittal information.

New Business

19.1 XX

2.16.2021 – XXX

Please notify  of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 23 Feb 2021 17:18:11 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 2.23.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda -20.docx
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 16, 2021 9:53 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 2, 2021 1:12 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.



Meeting Agenda

Job: ICE Building – Fitout
Location: 40 Manson Libby Road (b)(6); (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340 (b)(6); (b)(7)(C)

Date: 2/23/2021
Meeting: 20

Attendees
(b)(6); (b)(7)(C)

Item	Description
------	-------------

Regular Business

- 0.1 Current Work & Quality –Discuss upcoming inspections and non-conforming work if any**
Interior CMU walls are being constructed for the sally port and processing area. The drywallers have delivered their materials and are beginning with the demising wall. HVAC, Plumbing and Electrical rough ins are also being installed.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
We will continue with all the work noted above.
The updated schedule has been provided. GSA in-wall inspection is Friday 3/12 and furniture measuring on Monday 4/12. Substantial completion 5/14 with final completion on 6/4.
- 0.3 RFI’s – Review log and discuss potential for new items**
RFI 043 - Landscaping
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 102113_Toilet Compartments_001
 - 220500_Misc Plumbing_001
 - 329200_Turf_001
 - Appenidx E_Building Signage_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Future Change Orders
 - RFC 15 – February Winter Conditions
 - RFC No 16 - Time Extension



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

0.6 ASI/SKs – Review potential changes to the contract documents
None

0.7 Payment Application – Review pencil requisition, submission, and payment status
Req 6 will be sent by March 5th. The req review meeting is Tuesday 3/9 at 1:30.

Old Business

18.2 (b)(5); (b)(7)(E)

A large rectangular area of the document is completely redacted with a solid black fill, obscuring all text and graphics underneath.

New Business

20.1 (b)(5)

A large rectangular area of the document is completely redacted with a solid black fill, obscuring all text and graphics underneath.

Please notify (b)(6); (b)(7)(C) of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 2 Mar 2021 14:01:19 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 3.01.2021_40A Manson Libby Road - GSA Fitout - Meeting Agenda -21.pdf
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 12:18 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 16, 2021 9:53 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Meeting Agenda
Importance: High

Attached please find meeting agenda for our meeting today.



Meeting Agenda

Job: ICE Building – Fitout
Location: 40 Manson Libby Road (b)(6); (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340 (b)(6); (b)(7)(C)

Date: 3/1/2021
Meeting: 21

Attendees
(b)(6); (b)(7)(C)

Item	Description
------	-------------

Regular Business

- 0.1 **Current Work & Quality –Discuss upcoming inspections and non-conforming work if any**
Interior CMU walls are being constructed for the sally port and processing area. The drywallers have installed the [redacted] and are starting interior framing. HVAC, Plumbing and Electrical rough ins are also being installed.
- 0.2 **Schedule – Review master schedule and discuss planned activities for the next two weeks**
We will continue with all the work noted above.
GSA security inspection Monday 3/8 10am
GSA in-wall inspection is Friday 3/19.
- 0.3 **RFI’s – Review log and discuss potential for new items**
RFI 043 - Landscaping
- 0.4 **Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 220500_Misc Plumbing_001 – has been out since 1/21, we need this back asap
 - 329200_Turf_001 – has been out since 10/29, we need this back asap
 - Appenidx E_Building Signage_001
- 0.5 **Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - Change Orders
 - RFC 15 – February Winter Conditions
 - RFC No 16 - Time Extension
- 0.6 **ASI/SKs – Review potential changes to the contract documents**
None



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

0.7 Payment Application – Review pencil requisition, submission, and payment status
Req 6 will be sent by March 5th. The req review meeting is Tuesday 3/9 at 1:30.

Old Business

New Business

21.1 XXX
3.1.2021 –

Please notify (b)(6); (b)(7)(C) of any errors or omissions to the notes within (2) business days.

From: (b)(6); (b)(7)(C)
Sent: 29 Dec 2020 16:59:39 +0000
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - Meeting Agenda
Attachments: 12.29.2020_40A Manson Libby Road - GSA Fitout - Meeting Agenda-12.pdf, 40 Manson Libby_Schedule 12.28.2020.pdf
Importance: High

Attached please find meeting agenda and schedule for our meeting today.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 15, 2020 1:08 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: FW: ICE Scarborough ME - 12.11.20 Meeting Agenda

FYI, see attached agenda for today's meeting.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, December 15, 2020 11:53 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: ICE Scarborough ME - 12.11.20 Meeting Agenda

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

Attached is the meeting agenda for today's meeting.

Thanks,

(b)(6); (b)(7)(C)

Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275 (b)(6);
(b)(7)(C)



Meeting Agenda

Job: ICE Building – Fitout (b)(6); (b)(7)(C)
Location: 40 Manson Libby Road (b)(7)(C) Scarborough ME 04074
Meeting #: Teleconference – 505.340 (b)(6); (b)(7)(C)

Date: 12/29/2020
Meeting: 12

Attendees

(b)(6); (b)(7)(C)

Item	Description
------	-------------

Regular Business

- 0.1 Current Work & Quality – Discuss upcoming inspections and non-conforming work if any**
The scaffolding is being erected inside the building.
The site contractor has cleaned up the site for the season and de-mobilized.
The demolition crew, roofers and masons are set to start work on Monday the 4th.
- 0.2 Schedule – Review master schedule and discuss planned activities for the next two weeks**
A revised schedule has been provided.
- 0.3 RFI’s – Review log and discuss potential for new items**
RFI 028 - Gas Meter Pad
- 0.4 Submittals – Review log and identify new, pending, and overdue submittals**
Currently submittals with WRBC:
 - 01_Appendix A_Security_001
 - 220000_Oil Water Seperator_001
 - 329200_Turf_001
 - Appenidx E_Building Signage_001
- 0.5 Requests for Change– Review and discuss changes to the work that may have a cost impact**
 - RFC 04 – Addendum 8 & 9 changes – sent 11/2
 - WBRC has sent the GSA official change order to [redacted] on 12/23.
 - Future Change Orders
 - Winter Conditions
 - RFI 032 - Demising Wall CL 4



0.6 ASI/SKs – Review potential changes to the contract documents
None

0.7 Payment Application – Review pencil requisition, submission, and payment status
Req 3 is pending until RFC 04 is approved. Req 4 will be sent by 1/8.

Old Business

9.1 Winter Conditions

12.8.2020 - The original schedule, when the project was bid, was to take place in the summer months. Now that the project is being completed in the winter, there will be several costs implications and additional work needed.

- The first instance of this is the additional engineering for the scaffolding for the exterior walls. Since the scaffolding will be holding a potential snow load, they require additional engineering and potentially additional labor and materials. The cost of engineering is \$2875, while labor and materials are TBD.
- GFC also anticipates tenting for the masonry work. This will require additional labor and materials to protect the masonry installation. This cost is TBD.
- GFC also plans to rent a large heater to heat the existing area and tented masonry areas. It is GFCs intent to hook up to the existing building gas to run this heater, so the cost of the fuel will be billed directly to the owner. The anticipated cost of the heater for several months is \$3000.
- GFC will also be renting a snow bucket to clean up around our site areas the snow plow contractor is unable to get to, due to construction. The cost is TBD.
- GFC would like to suggest that they advise of any large costs for winter conditions as they come up. Otherwise, GFC will track all winter condition costs for the month and provide a change order with each requisition for that month.

12.15.2020 – GSA and the owners will be discussing this after the call.

12.21.2020 - Budget numbers for winter conditions. This is all dependent on the weather, the more snow and cold we get, the more or less everything could be.

- Scaffolding Engineering - \$3210
- Heater and Fuel = \$10,000-\$20,000
- Tenting = \$8000-\$13,000
- Snow Bucket and snow removal - \$2000-\$3000
- Interior Heater - TBD

Just to clarify, we found that the heater to hook up to the owners fuel was not the best option. We will be renting a propane heater and getting a tank from Suburban Propane delivered to site.

We will be getting an indirect heater, to heat the interior, which will be hooked up to the owners gas, we do not know the costs for that yet.

GFC will be keeping all slips for all winter work and provide as a back up with the change orders.

12.29.2020 -



20 Mechanic Street
Gorham, ME 04038
PH : 207-839-2744

New Business

101.1 None
12.28.2020 - None

Please notify (b)(6), (b)(7)(C) of any errors or omissions to the notes within (2) business days.



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
1	Preconstruction	137 days	Wed 5/13/20	Thu 11/19/20	
8	Mobilization	4 days	Fri 11/6/20	Wed 11/11/20	
13	Sitework	34 days	Mon 11/9/20	Thu 12/24/20	
30	Site Completion	TBD	TBD	TBD	
31	Site Demo & Removal	TBD	TBD	TBD	
32	Box cut parking area	TBD	TBD	TBD	
33	Gravel & Grade	TBD	TBD	TBD	
34	Install Fencing	TBD	TBD	TBD	
35	Remaining Bollards	TBD	TBD	TBD	
36	Curbing	TBD	TBD	TBD	
37	Binder Pave	TBD	TBD	TBD	
38	Landscaping	TBD	TBD	TBD	
39	Finish Pave	TBD	TBD	TBD	
40	Signage & Markings	TBD	TBD	TBD	
41	Foundations	20 days	Thu 11/19/20	Wed 12/16/20	
42	Form Footings	2 days	Thu 11/19/20	Fri 11/20/20	19FS-1 day
43	Rebar Inspection	1 day	Fri 11/20/20	Fri 11/20/20	42FS-1 day
44	Place Footers	1 day	Fri 11/20/20	Fri 11/20/20	43FS-1 day
45	Form Walls	2 days	Mon 11/23/20	Tue 11/24/20	44
46	Rebar Inspection	1 day	Wed 11/25/20	Wed 11/25/20	45
47	Place Walls	1 day	Wed 11/25/20	Wed 11/25/20	46FS-1 day
48	Prep Entry Slabs	3 days	Wed 12/2/20	Fri 12/4/20	
49	Rebar Inspection	1 day	Fri 12/4/20	Fri 12/4/20	48FS-1 day
50	Place Entry Slabs	1 day	Fri 12/4/20	Fri 12/4/20	49FS-1 day
51	Form Site Slabs	3 days	TBD	TBD	50
52	Rebar Inspection	1 day	TBD	TBD	51FS-1 day
53	Place Site Slabs	2 days	TBD	TBD	52FS-1 day
54	Interior Demolition	5 days	Wed 9/16/20	Tue 9/22/20	
58	Underslab Activities	26 days	Mon 11/9/20	Mon 12/14/20	
59	Trenching	1 day	Mon 11/9/20	Mon 11/9/20	5
60	Plumbing Rough	6 days	Tue 11/17/20	Tue 11/24/20	59FS+5 days
61	OWS installation	2 days	Tue 11/24/20	Wed 11/25/20	
62	Electrical Rough in	3 days	Mon 11/23/20	Wed 11/25/20	6FS+1 day
63	Plumbing & Electrical Inspection	1 day	Mon 11/30/20	Mon 11/30/20	62
64	Backfill	4 days	Tue 12/1/20	Fri 12/4/20	63
65	Slab Prep	2 days	Mon 12/7/20	Tue 12/8/20	64FS-1 day
66	Pour Interior Slabs	2 days	Wed 12/9/20	Thu 12/10/20	64
67	Break Results wait time	2 days	Fri 12/11/20	Mon 12/14/20	66
68	Break Test Results	1 day	Mon 12/14/20	Mon 12/14/20	
69	Exterior Wall Demo	29 days	Tue 12/15/20	Fri 1/22/21	
70	Engineering	7 days	Tue 12/15/20	Wed 12/23/20	68



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

ID	Task Name	Duration	Start	Finish	Predecessors
71	Shoring	8 days	Tue 12/22/20	Thu 12/31/20	70FS-2 days
72	Roofing Demo	4 days	Mon 1/4/21	Thu 1/7/21	71FS-1 day
73	Exter wall Demo	15 days	Mon 1/4/21	Fri 1/22/21	71FS-1 day
74	Masonry	25 days	Mon 1/4/21	Fri 2/5/21	
75	Ext CMU	25 days	Mon 1/4/21	Fri 2/5/21	73FS-10 days
76	Int CMU	20 days	Mon 1/11/21	Fri 2/5/21	75FS-20 days
77	Exterior Openings & Roofing	28 days	Mon 1/4/21	Wed 2/10/21	
78	Sectional Doors	5 days	Mon 2/1/21	Fri 2/5/21	
79	Storefronts & Windows	3 days	Mon 2/8/21	Wed 2/10/21	
80	Roofing	25 days	Mon 1/4/21	Fri 2/5/21	
81	Interior Fit Up	86 days	Thu 12/17/20	Thu 4/15/21	
82	HVAC Duct & RTU penetrations	13 days	Mon 1/11/21	Wed 1/27/21	
83	Cable tray	13 days	Mon 1/11/21	Wed 1/27/21	
84	CMU Wall Pathways/MEP coordinatic	20 days	Mon 1/11/21	Fri 2/5/21	
85	LGMF & Door Frames	18 days	Wed 1/13/21	Fri 2/5/21	75FS-18 days
86	Blocking	13 days	Wed 1/13/21	Fri 1/29/21	
87	MEP & Comm/Security Rough	13 days	Wed 1/20/21	Fri 2/5/21	85FS-13 days
88	MEP Inspection	1 day	Fri 2/5/21	Fri 2/5/21	
89	GSA In Wall Inspection	0 days	Fri 2/5/21	Fri 2/5/21	87
90	Insulation & Drywall	20 days	Mon 2/8/21	Fri 3/5/21	89
91	GSA Field Measure - Furniture	0 days	Fri 3/5/21	Fri 3/5/21	90
92	Prime & First Coat Paint	10 days	Mon 3/8/21	Fri 3/19/21	90
93	Ceiling Grid & Cuts	10 days	Mon 3/22/21	Fri 4/2/21	92
94	MEP Finishes	12 days	Mon 3/22/21	Tue 4/6/21	92
95	Flooring	10 days	Mon 3/22/21	Fri 4/2/21	92
96	Casework	3 days	Mon 3/22/21	Wed 3/24/21	92
97	Flood Ceilings	5 days	Wed 4/7/21	Tue 4/13/21	94
98	Specialites & Furnishings	7 days	Mon 4/5/21	Tue 4/13/21	95
99	Doors & Hardware	7 days	Mon 4/5/21	Tue 4/13/21	95
100	Final Paint	7 days	Mon 4/5/21	Tue 4/13/21	95
101	Signage	1 day	Fri 4/9/21	Fri 4/9/21	100FS-3 days
102	Cleaning	3 days	Tue 4/13/21	Thu 4/15/21	101
103	Substantial Completion	0 days	Thu 4/15/21	Thu 4/15/21	102
104	Closeout	11 days	Fri 4/16/21	Fri 4/30/21	
105	Punchlist	10 days	Fri 4/16/21	Thu 4/29/21	103
106	Final Inspection - GSA	1 day	Fri 4/30/21	Fri 4/30/21	105
107	Occupancy & Turnover	0 days	Fri 4/30/21	Fri 4/30/21	106



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

Resource Names	March		April			May			June			July			August			September			October			November	
	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	
Great Falls Construction																									
Great Falls Construction																									
Woods Excavating																									
Hy Tech Plumbing																									
Woods Excavating																									
Concrete Craftsman																									



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

Resource Names	March			April			May			June			July			August			September			October			November
	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	B
Seacoast Scaffolding																									
Franks Demo																									
Giroux Family Masonry																									
Giroux Family Masonry																									
Overhead Door																									
Glass Solutions																									
Glidden Roofing																									
Lapointe Drywall,Kelly Bros																									
East Coast Electrical,HVAC Service																									
Lapointe Drywall																									
NE Painting																									
Landy & Son																									
East Coast Electrical,HVAC Service																									
Triform,Hascall & Hall																									
Chilton Cabinetmakers																									
Landry & Son Acoustics																									
Material Handling Sales,Decoratin																									
Great Falls Construction,Kelly Bros																									
NE Painting																									
Welch Signs																									
All Contractors																									




6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
Scarborough ME 04074
GSA Fitout

November			December			January			February			March			April			May			June			July			August			September		
B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E			

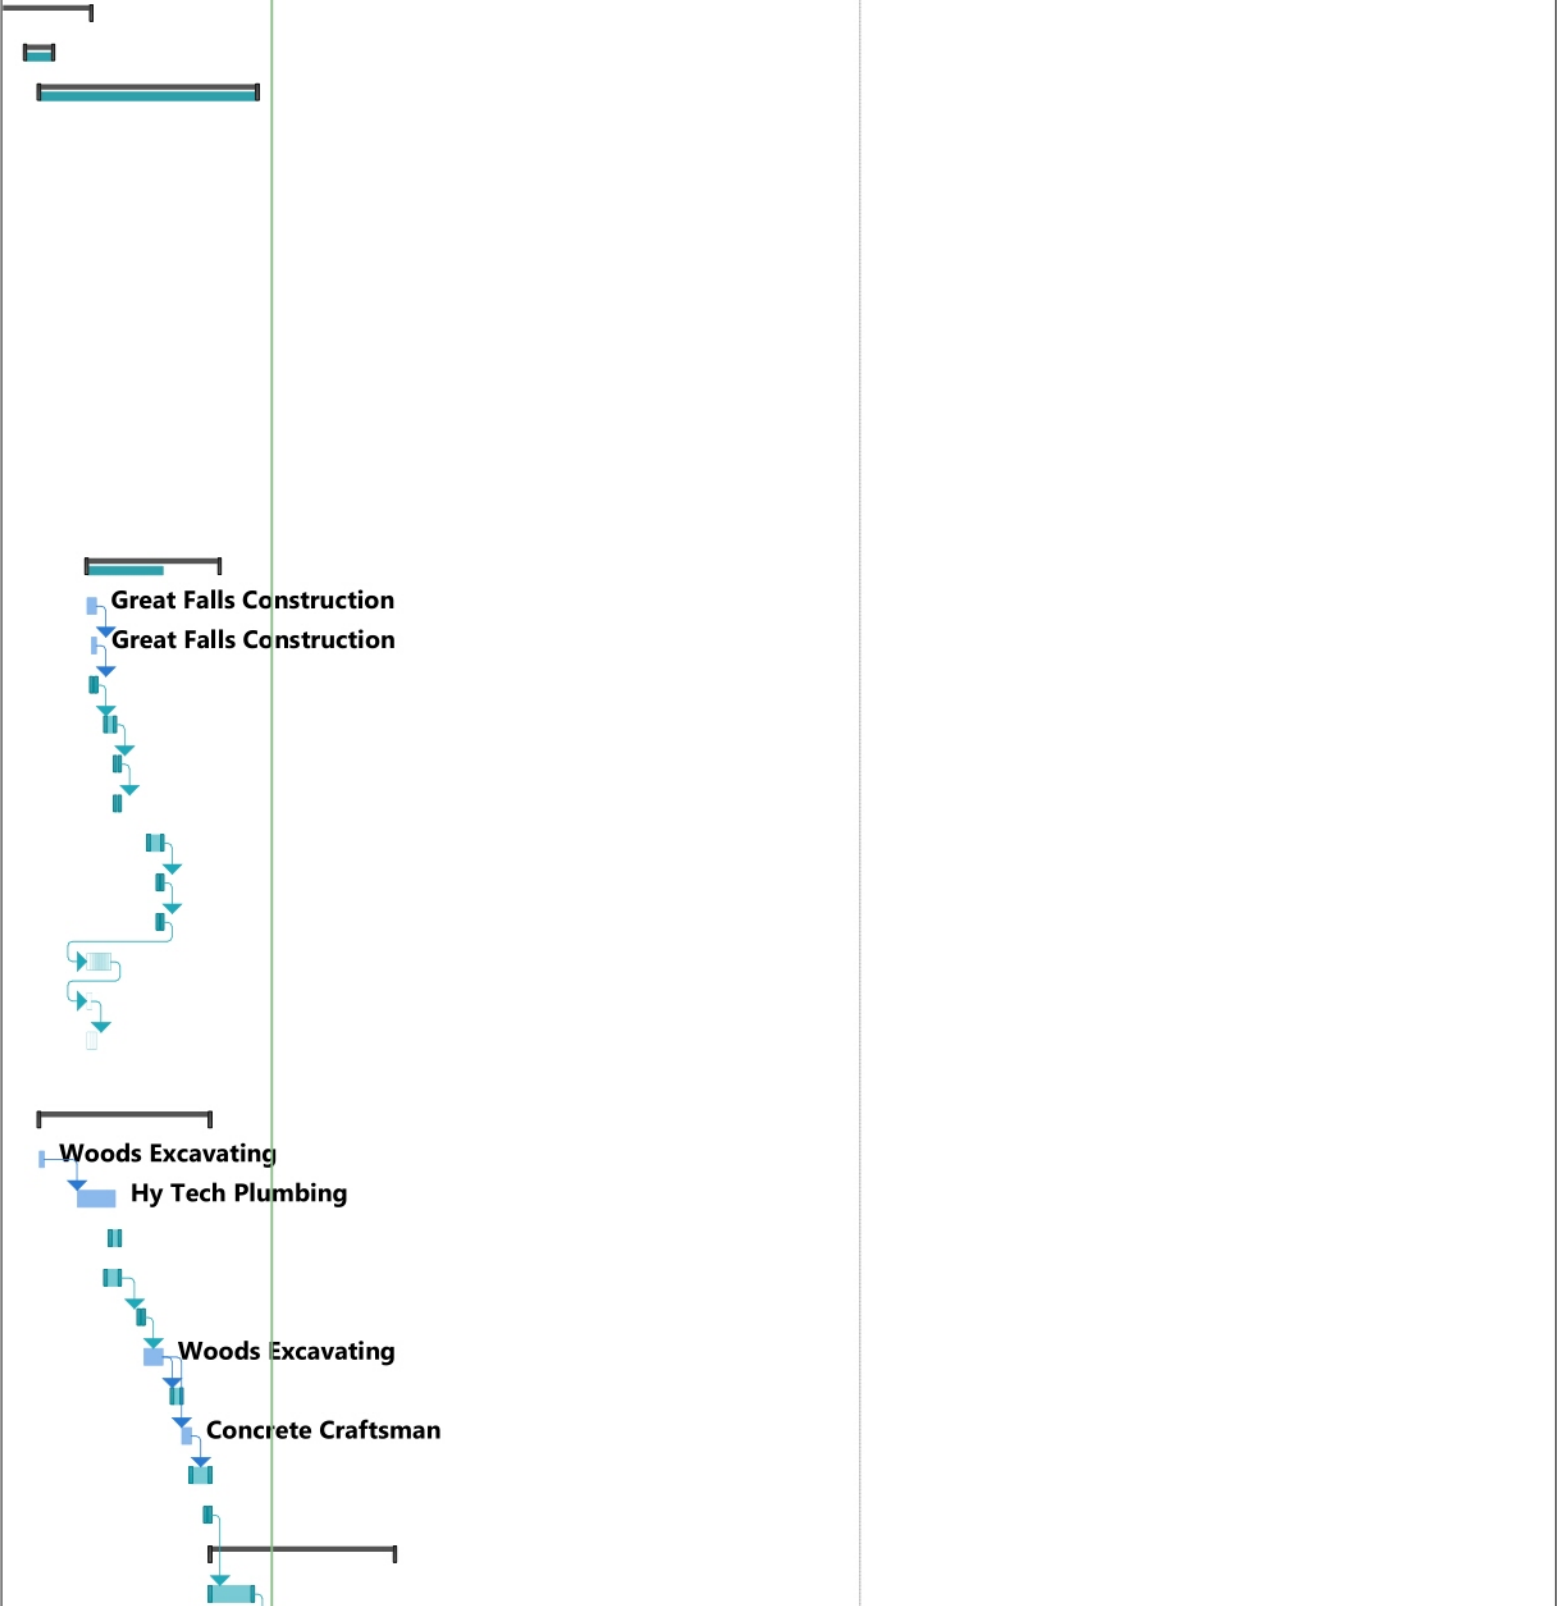




Construction Schedule

40A Manson Libby Road
 Scarborough ME 04074
 GSA Fitout

6,080 SF Renovation

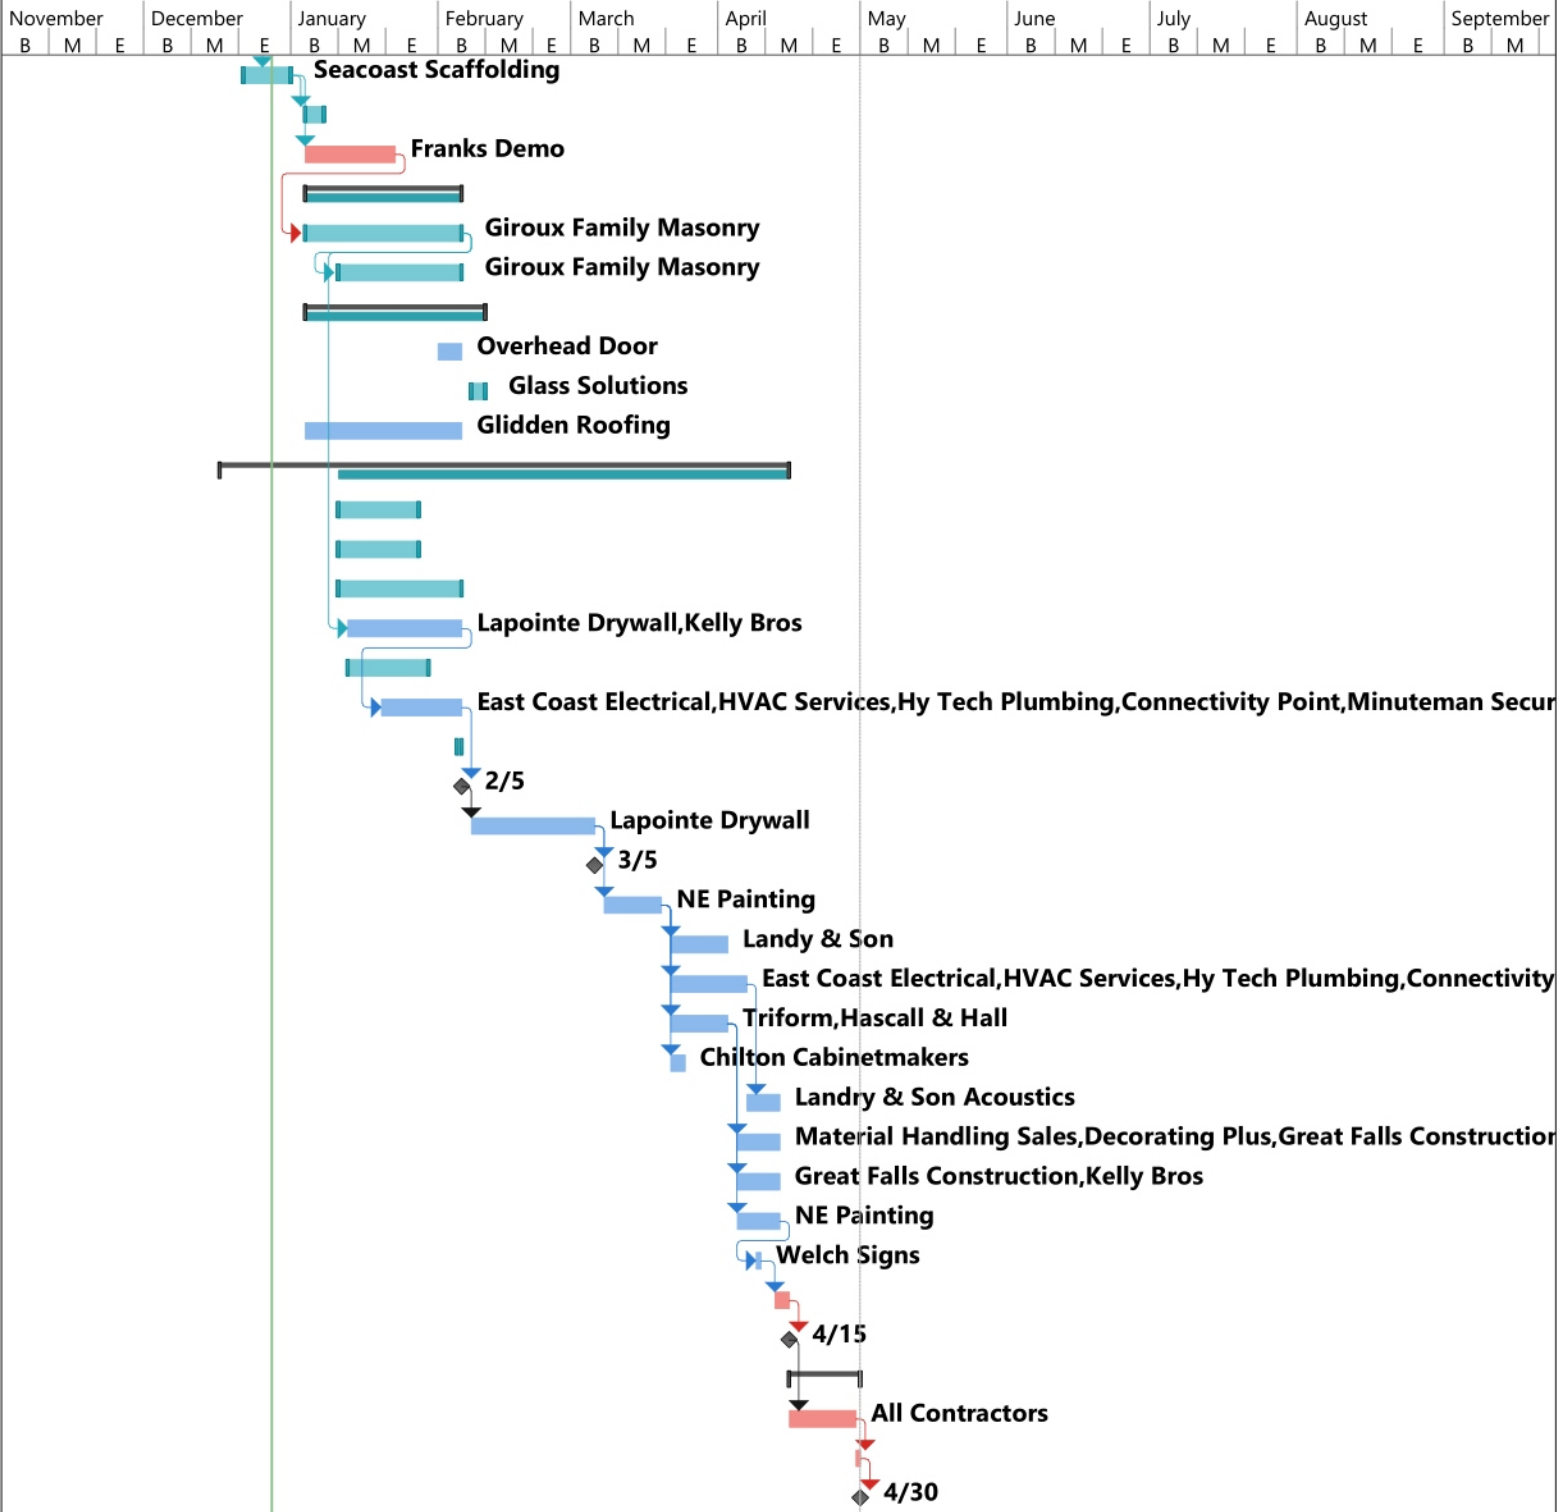



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
Scarborough ME 04074
GSA Fitout

Table with 12 columns representing months from October to August, each with sub-columns for days of the week (E, B, M).

Main empty grid area for the construction schedule.



6,080 SF Renovation

Construction Schedule

40A Manson Libby Road
Scarborough ME 04074
GSA Fitout

r	October			November			December			January			February			March			April			May			June			July			August
	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E

<p>curity</p> <p>ity Point,Minuteman Security</p> <p>ion,Thompson & Anderson</p>																														
--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

From: (b)(6); (b)(7)(C)
Sent: 24 Mar 2021 12:04:28 +0000
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)

Subject: RE: ICE Scarborough ME - Move/Disposal of items from 176 Gannett Drive TO 40 Mason Libby Rd. Scarborough
Attachments: RE_ ERO_HSI Disposal of items from 176 Gannett Drive .pdf
Importance: High

Good morning (b)(6); (b)(7)(C)

Is tomorrow morning at 10:30 am a good time for (b)(6) to go there? Is the list ready? Please confirm.

I got a confirmation from HSI that everything inside HSI space is ok to be disposed of. See email confirmation attached.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, March 24, 2021 7:45 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: Re: ICE Scarborough ME - Move/Disposal of items from 176 Gannett Drive TO 40 Mason Libby Rd. Scarborough

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

I was planning to go to the field office tomorrow morning at 10:30 am. Yes you will need a RWA and list of items that are going to a new location and what has been disposed of. Please let me know if tomorrow morning is a problem.

Joe

On Tue, Mar 23, 2021 at 1:28 PM (b)(6); (b)(7)(C) wrote:

Hi (b)(6); (b)(7)(C)

Have you been able to meet with the field office? Is there anything that you are waiting from us?
I need an RWA to process the funds.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, March 10, 2021 8:38 AM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: ICE Scarborough ME - Move/Disposal of items from 176 Gannett Drive TO 40 Mason Libby Rd. Scarborough

Good morning (b)(6); (b)(7)(C)

Since you are going to the site today at 11:30 am, could you please meet with the field office about the moving and disposal of all the items at ERO space as well as the empty HSI space?
Remember, I need an RWA with sufficient time to process the moving cost and get it approved.

Please let me know if you have any questions.

Thank you,

(b)(6); (b)(7)(C)

MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

--

Thanks,

(b)(6); (b)(7)(C)

Property Manager
U.S. General Services Administration

T J McIntyre Federal Building
80 Daniel Street
Portsmouth NH 03801

Office: (603) 433-(b)(6);
Cell: (603) 566-(b)(7)(C)

Fax: (603) 433-0578

(b)(6), (b)(7)(C)

**FOR INFORMATION ON GSA RESPONSE TO COVID-19
(CORONAVIRUS) PLEASE VISIT: [GSA COVID19 FAQ](#)**

From: (b)(6); (b)(7)(C)
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ERO/HSI Disposal of items from 176 Gannett Drive
Date: Tuesday, March 23, 2021 6:42:11 PM

Good Afternoon,

I just confirmed you can dispose anything left over.

Thanks,

(b)(6);
(b)(7)(C)

(b)(6); (b)(7)(C)
Mission Support Specialist
Homeland Security Investigations
Boston, MA
Cell: (617) 272- (b)(6); (b)(7)(C)
FAX (617) 565-7422
Email: (b)(6); (b)(7)(C)
[HSI Boston SharePoint](#)

-----Original Message-----

From: (b)(6); (b)(7)(C)
Sent: Tuesday, March 23, 2021 1:46 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: ERO/HSI Disposal of items from 176 Gannett Drive
Importance: High

Good afternoon (b)(6); (b)(7)(C)

ERO is moving from 176 Gannett Drive very soon. Does HSI have anything left inside 176 Gannett Drive? If HSI still has anything in there, it needs to be pick up soon, otherwise, it will be disposed of. Please let us know.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6); (b)(7)(C)
C: 202-754 (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 23 Feb 2021 19:46:11 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

Yes, 03/03/2021

Thank you,

(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O: 305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 2:29 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)

10 a.m. March 3rd?

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 2:28 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

(b)(6);
(b)(7)(C)

The partial inspection is going to be next Wednesday 03 in the morning (7-12pm). What time will you be there?

(b)(6); (b)(7)(C) please coordinate with the GC the time that you will be arriving. (b)(6); (b)(7)(C) phone number 207-615 (b)(6); (b)(7)(C) Below his information.

(b)(6); (b)(7)(C)

Project Manager

(b)(6); (b)(7)(C)



Great Falls Construction

20 Mechanic Street
Gorham, ME 04038


O: (207) 839-
C: (207) 615-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 11:57 AM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - (b)(7)(E)
Importance: High

Yes,

(b)(7)(E)



Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-
C: 202-754-

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 11:46 AM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - (b)(7)(E)

Perfect (b)(6); (b)(7)(C); (b)(5)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 11:45 AM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

Any time during Wednesday and Thursday?

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager

O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 11:41 AM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - (b)(7)(E)

Just found out I have another meeting today at the same time as the ERO Scarborough time. So I wont be on call. I can do the inspection Wednesday or Thursday. Let me know

From: (b)(6); (b)(7)(C)
Sent: Friday, February 19, 2021 12:24 PM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

Super! They are going to discuss the date and time in our meeting next Tuesday. Can you please attend the construction meeting next Tuesday?

Thank you,
(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597
C: 202-754

From: (b)(6); (b)(7)(C)
Sent: Friday, February 19, 2021 12:21 PM
To: (b)(6); (b)(7)(C)
Subject: RE: ICE Scarborough ME - (b)(7)(E)

(b)(5); (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Friday, February 19, 2021 12:14 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: FW: ICE Scarborough ME (b)(7)(E)

Good morning (b)(6); (b)(7)(C)

Will you be able to assist me in the first wall inspection next week? Please see request below.

Thank you,
(b)(6); (b)(7)(C)

MA, NCARB, SAME, Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597 (b)(6);
C: 202-754 (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Friday, February 19, 2021 11:09 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: ICE Scarborough ME - Security Mesh Inspection

CAUTION: This email originated from outside of DHS. DO NOT click links or open attachments unless you recognize and/or trust the sender. Contact [ICE SOC SPAM](#) with questions or concerns.

Hi (b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)
The installers will start the work next week. We will confirm the date and time when they will be ready for the first inspection at next week's meeting (2/23/2021).

Thanks,

(b)(6); (b)(7)(C)
Project Manager
New England Region
U.S. General Services Administration
10 Causeway Street, (b)(6); (b)(7)(C)
Boston, MA 02222
(C) 617-275 (b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: 23 Feb 2021 20:07:25 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

Thank you for your cooperation.

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 2:47 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)

No problem

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 2:46 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)
Importance: High

Yes, 03/03/2021

Thank you,

(b)(6); (b)(7)(C)
MA. NCARB. SAME. Intl. Assoc. AIA.
Regions 1-2 & 4 | OAFM Project Manager
O:305-597-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, February 23, 2021 2:29 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: ICE Scarborough ME (b)(7)(E)

10 a.m. March 3rd?

From: (b)(6); (b)(7)(C)
Sent: 30 Oct 2018 14:52:18 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 75 John Roberts Building C- ERO South Portland
Attachments: EMOP C GSA-ERO 5,188 SF.PDF
Importance: High

Good Morning (b)(6); (b)(7)(C)

(b)(5)

Call me at my cell if you have any questions or concerns.

Thank you,

(b)(6); (b)(7)(C)
Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, October 29, 2018 5:50 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Let you know when I hear back from GSA.

Thank you,

(b)(6); (b)(7)(C)
Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, October 29, 2018 5:29 PM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 75 John Roberts Building C- ERO South Portland

Works for me.

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Monday, October 29, 2018 5:27 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

(b)(6); (b)(7)(C)

After I looked into airplanes schedules, 11 am is not possible for me to get there on time. I can be there at 1:00pm on Thursday.
Would this be a problem for you?

Thank you,

(b)(6); (b)(7)(C)
Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, October 29, 2018 1:43 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Confirmed! 11 am will be perfect. See you there.

Thank you,

(b)(6); (b)(7)(C)

Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, October 29, 2018 1:31 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: 75 John Roberts Building C- ERO South Portland

Would 11 AM work?

(b)(6); (b)(7)(C) SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6);
(b)(7)(C)
Desk Phone#: 207-80-(b)(6);
(b)(7)(C)
Cell Phone#: 207-252-(b)(6);
(b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)

Date: Monday, Oct 29, 2018, 13:20

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6);
(b)(7)(C)

What time is convenient for you?

Thank you,

(b)(6); (b)(7)(C)

Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-(b)(6);

From: (b)(6); (b)(7)(C)
Sent: Friday, October 26, 2018 11:27 AM
To: (b)(6); (b)(7)(C)
Cc: [REDACTED]
Subject: RE: 75 John Roberts Building C- ERO South Portland

Does next Thursday work?

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-25-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Thursday, October 25, 2018 8:37 AM
To: (b)(6); (b)(7)(C)
Cc: [REDACTED]
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Good Morning (b)(6); (b)(7)(C)



Thank you,

(b)(6); (b)(7)(C)
Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD | OAFM | DHS | ICE
500 12th Street SW
Washington, DC 20536

C:202-754 (b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, October 18, 2018 9:44 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High



From: (b)(6); (b)(7)(C)
Sent: Thursday, October 18, 2018 9:37 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(5)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-808-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)
Sent: Thursday, October 18, 2018 9:29 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Good morning

(b)(6);
(b)(7)(C)

(b)(5)

Thank you,

(b)(6); (b)(7)(C)

Facilities Management Division (FMD)
Office of Asset and Facilities Management (OAFM)
FMD|OAFM|DHS|ICE
500 12th Street SW
Washington, DC 20536
C:202-754-

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Thursday, October 18, 2018 9:15 AM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: 75 John Roberts Building C- ERO South Portland

Good morning

(b)(6); (b)(7)(C)

(b)(5)

(b)(6); (b)(7)(C)

SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-

(b)(6);
(b)(7)(C)

Desk Phone#: 207-808-

(b)(6);
(b)(7)(C)

Cell Phone#: 207-252-

Fax#: 207-780-3216

~~Warning: This document is UNCLASSIFIED//FOR OFFICIAL USE ONLY (U//FOUO). It contains information that may be exempt from public release under the Freedom of Information Act (5 U.S.C. 552). It is to be controlled, stored, handled, transmitted, distributed, and disposed of in accordance with DHS policy relating to FOUO information and is not to be released to the public or other personnel who do not have a valid "need-to-know" without prior approval of an authorized DHS official. No portion of this report should be furnished to the media, either in written or verbal form.~~

From: (b)(6); (b)(7)(C)

Sent: Monday, September 24, 2018 7:03 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High



From: (b)(6); (b)(7)(C)
Sent: Monday, September 24, 2018 6:55 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(5)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Date: Monday, Sep 24, 2018, 18:34
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)



Call me tomorrow to explain.

Thank you,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 24, 2018 5:09 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)

Here are some of the photos you asked for.

(b)(5); (b)(7)(E)

I would suggest the public entrance face the same direction as the current entrance for the Insurance Company.

I will sketch something out tomorrow as you requested.

It might work, with minimum disruption for the other tenants.

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Date: Monday, Sep 24, 2018, 16:53
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Hi (b)(6); (b)(7)(C)

FYI, below my email to GSA after my meeting with (b)(6); (b)(7)(C) today.

(b)(5); (b)(7)(E)

Let you know when I get a response from GSA,

Thank you,

(b)(6); (b)(7)(C)

Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-
C: 202-754-

From: (b)(6); (b)(7)(C)

Sent: Monday, September 24, 2018 12:06 PM

To: (b)(6); (b)(7)(C)

Cc:

Subject: RE: 75 John Roberts Building C- ERO South Portland

Importance: High

Good Morning (b)(6); (b)(7)(C)

(b)(5)



Let you know later my conversation with my supervisor about GSA email.

Thank you,
(b)(6); (b)(7)(C)

Region 1 - Lead Architect
FMD|OAFM|DHS|ICE

500 12th St SW
Washington, DC 20536
O: 202-732-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 17, 2018 8:26 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Good morning,

(b)(5)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-800-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Date: Monday, Sep 17, 2018, 08:23
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Good Morning (b)(6); (b)(7)(C)

(b)(5)

[REDACTED]

I will keep you informed.

Thank you,

(b)(6); (b)(7)(C)

Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-^{(b)(6);}
^{(b)(7)(C)}
C: 202-754-^{(b)(6);}
^{(b)(7)(C)}

From: (b)(6); (b)(7)(C)

Sent: Friday, September 14, 2018 11:29 AM

To: (b)(6); (b)(7)(C)

Cc: [REDACTED]

(b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

I actually just drove by the building. They are already putting up the large fence and have knocked holes in the walls for doors and the sallyport it appears.

(b)(6); (b)(7)(C) SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-^{(b)(6);}
^{(b)(7)(C)}

Desk Phone#: 207-808-^{(b)(6);}
^{(b)(7)(C)}

Cell Phone#: 207-252-^{(b)(6);}
^{(b)(7)(C)}

Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)

Date: Friday, Sep 14, 2018, 10:46

To: (b)(6); (b)(7)(C)

Cc: [REDACTED]

(b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

Good morning,

Just wondering if we have any update on the building?

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-800-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Date: Tuesday, Aug 21, 2018, 12:55
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C); (b)(5); (b)(7)(E)

(b)(6); (b)(7)(C) RA
Deputy Unit Chief – Facilities East
DHS | ICE | OAFM
500 12th St SW
Washington, DC
O: 202-731-(b)(6); (b)(7)(C)
C: 202-903-(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, August 21, 2018 12:53 PM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(5); (b)(7)(E)

(b)(6);
(b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Monday, August 20, 2018 8:12 AM

To: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Cc: (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6);
(b)(7)(C)

I'm including (b)(6); (b)(7)(C) here. He is the better one to speak to this.

(b)(6); (b)(7)(C)

RA

Deputy Unit Chief – Facilities East

DHS | ICE | OAFM

500 12th St SW

Washington, DC

O: 202-732 (b)(6);

C: 202-903 (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Friday, August 17, 2018 10:50 AM

To: (b)(6); (b)(7)(C)

Cc:

(b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)

(b)(5); (b)(7)(E)

Thanks,

(b)(6); (b)(7)(C)

SDDO

ICE ERO Portland, ME Sub-Office

176 Gannett Drive

South Portland, ME 04106

Main Office Phone#: 207-780-^{(b)(6);}
^{(b)(7)(C)}
Desk Phone#: 207-800-^{(b)(6);}
^{(b)(7)(C)}
Cell Phone#: 207-252-^{(b)(6);}
^{(b)(7)(C)}
Fax#: 207-780-3216

From: ^{(b)(6); (b)(7)(C)}
Sent: Thursday, August 16, 2018 12:40 PM
To: ^{(b)(6); (b)(7)(C)}
Cc: ^{(b)(6); (b)(7)(C)}
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Hello ^{(b)(6);}
^{(b)(7)(C)}

Attached please find the tentative draft schedule up to occupancy.

Thank you,

^{(b)(6); (b)(7)(C)}
Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-^{(b)(6);}
C: 202-754-^{(b)(7)(C)}

From: ^{(b)(6); (b)(7)(C)}
Sent: Thursday, August 16, 2018 12:11 PM
To: ^{(b)(6); (b)(7)(C)}
^{(b)(6); (b)(7)(C)}
Cc: ^{(b)(6); (b)(7)(C)}
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

I will be sending the test to GSA right now.

Thank you,

^{(b)(6); (b)(7)(C)}

From: ^{(b)(6); (b)(7)(C)}
Sent: Thursday, August 16, 2018 11:34 AM
To: ^{(b)(6); (b)(7)(C)}
^{(b)(6); (b)(7)(C)}
Cc: ^{(b)(6); (b)(7)(C)}
Subject: RE: 75 John Roberts Building C- ERO South Portland

As the initial draft, looks good. Thanks!

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-808-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Sent: Thursday, August 16, 2018 11:24 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Looks good!

Thanks!

(b)(6); (b)(7)(C) PMP
East Region Branch Chief, IT Field Operations Branch
IT Operations Division
Office of the Chief Information Officer
U.S. Immigration and Customs Enforcement
Department of Homeland Security
Office: (207) 808-(b)(6); (b)(7)(C)
Mobile: (207) 252-(b)(6); (b)(7)(C)
Email: (b)(6); (b)(7)(C)
ICE Service Desk: (888) 347-(b)(6); (b)(7)(C) or via web <https://servicedesk.ice.dhs.gov>

From: (b)(6); (b)(7)(C)
Sent: Thursday, August 16, 2018 11:10 AM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Good Morning (b)(6); (b)(7)(C)

(b)(6); (b)(7)(C)
Please discuss among yourselves and let me know ASAP, because we need to give an answer to GSA this afternoon.

Please call me if you have any questions or concerns.

Thank you,

(b)(6); (b)(7)(C)

Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Thursday, August 16, 2018 9:32 AM
To: (b)(6); (b)(7)(C)
(b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Hey (b)(6); (b)(7)(C)

Thanks!

(b)(6); (b)(7)(C)

PMP

East Region Branch Chief, IT Field Operations Branch
IT Operations Division
Office of the Chief Information Officer
U.S. Immigration and Customs Enforcement
Department of Homeland Security

Office: (207) 808-(b)(6); (b)(7)(C)

Mobile: (207) 252-(b)(6); (b)(7)(C)

Email: (b)(6); (b)(7)(C)

ICE Service Desk: (888) 347-(b)(6); (b)(7)(C) or via web <https://servicedesk.ice.dhs.gov>

From: (b)(6); (b)(7)(C)
Sent: Thursday, August 16, 2018 9:18 AM
To: (b)(6); (b)(7)(C)

Subject: FW: 75 John Roberts Building C- ERO South Portland
Importance: High

fyi

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-^{(b)(6);}_{(b)(7)(C)}
Desk Phone#: 207-80^{(b)(6);}_{(b)(7)(C)}
Cell Phone#: 207-252^{(b)(6);}_{(b)(7)(C)}
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Sent: Thursday, August 16, 2018 8:23 AM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Good Morning (b)(6);
(b)(7)(C)

To let you know that I am teleworking today. I can call you at 10am today.

Thank you,

(b)(6); (b)(7)(C)

C: 202-754-^{(b)(6);}_{(b)(7)(C)}

From: (b)(6); (b)(7)(C)
Sent: Wednesday, August 15, 2018 5:44 PM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Attached the requirements.

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, August 15, 2018 5:28 PM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

(b)(5)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, August 15, 2018 5:26 PM

To: (b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(5)

(b)(6); (b)(7)(C) SDDO

ICE ERO Portland, ME Sub-Office

176 Gannett Drive

South Portland, ME 04106

Main Office Phone#: 207-780-

(b)(6);
(b)(7)(C)

Desk Phone#: 207-80-

(b)(6);
(b)(7)(C)

Cell Phone#: 207-252-

Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)

Date: Wednesday, Aug 15, 2018, 5:23 PM

To: (b)(6); (b)(7)(C)

Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6);
(b)(7)(C)

(b)(5)

Please see attached and let me know what you think.

Thank you,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)

Sent: Wednesday, August 15, 2018 3:44 PM

To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

Will do.

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-800-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Date: Wednesday, Aug 15, 2018, 3:42 PM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)
(b)(5); (b)(6); (b)(7)(C)

Thank you,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, August 15, 2018 3:13 PM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)

(b)(5)

(b)(6); (b)(7)(C) SDDO
ICE ERO Portland, ME Sub-Office

176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Sent: Wednesday, August 15, 2018 2:32 PM
To: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Hi (b)(6); (b)(7)(C)

(b)(5)

Thank you,

(b)(6); (b)(7)(C)
Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-(b)(6); (b)(7)(C)
C: 202-754-(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Wednesday, August 15, 2018 1:42 PM
To: (b)(6); (b)(7)(C)
Subject: Automatic reply: 75 John Roberts Building C- ERO South Portland

Hello,

I am currently out of the office.

Please contact (a)SDDO (b)(6); (b)(7)(C) for assistance.


Thanks,

(b)(6); (b)(7)(C)

SDDO

ICE ERO Portland, ME Sub-Office
176 Gannett Driv
South Portland, ME 04106
Office#207-78
Cell# 207-252-

(b)(6);
(b)(7)(C)



From: (b)(6); (b)(7)(C)
Sent: 25 Sep 2018 18:41:40 +0000
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Hi (b)(6); (b)(7)(C)

(b)(5)

Please call me if you have any questions.

Thank you,

(b)(6); (b)(7)(C)

Region 1 - Lead Architect
FMD|OAFM|DHS|ICE
500 12th St SW
Washington, DC 20536
O: 202-732-(b)(6);
C: 202-754-(b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, September 25, 2018 9:10 AM
To: (b)(6); (b)(7)(C)
Cc:
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

Good Morning (b)(6); (b)(7)(C)

I am waiting for GSA response about the sketch.
Let you know later.

Best,

(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Tuesday, September 25, 2018 9:00 AM

To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)

(b)(5)

(b)(6); (b)(7)(C), SDDO
ICE ERO Portland, ME Sub-Office
176 Gannett Drive
South Portland, ME 04106

Main Office Phone#: 207-780-(b)(6); (b)(7)(C)
Desk Phone#: 207-80-(b)(6); (b)(7)(C)
Cell Phone#: 207-252-(b)(6); (b)(7)(C)
Fax#: 207-780-3216

From: (b)(6); (b)(7)(C)
Sent: Monday, September 24, 2018 6:35 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland
Importance: High

(b)(6); (b)(7)(C)
(b)(5)

Call me tomorrow to explain.

Thank you,
(b)(6); (b)(7)(C)

From: (b)(6); (b)(7)(C)
Sent: Monday, September 24, 2018 5:09 PM
To: (b)(6); (b)(7)(C)
Cc: (b)(6); (b)(7)(C)
Subject: RE: 75 John Roberts Building C- ERO South Portland

(b)(6); (b)(7)(C)

Here are some of the photos you asked for.
